

application and extended the construction deadline to February 7, 2001.

3. While the Archer City application was pending, Texas Grace encountered various difficulties, including health problems of its principal. On March 5, 1999 Texas Grace notified the staff of its belief that its construction deadline should be extended. It made this request in accordance with our new broadcast construction rules, which provide for tolling in limited circumstances. 47 C.F.R. § 73.3598(b). *See Report and Order*, MM Docket No. 98-43, 13 FCC Rcd 23056, 23090-93 (1998) ("*Streamlining R&O*"), *recon. granted in part and denied in part*, 14 FCC Rcd 17525 (1999) ("*Streamlining MO&O*"). On October 20, 2000, the staff denied Texas Grace's tolling request. Texas Grace filed a petition for reconsideration, which the staff denied on December 14, 2000. The staff concluded that none of the circumstances Texas Grace detailed -- health problems and various alleged permit "encumbrances" including rulemaking proceedings, related applications, and the amount of time the staff took to act on Texas Grace's initial tolling request -- were qualifying tolling events. The staff also held that Texas Grace was incorrect in its assertion that it was entitled under the Commission's rules to a new three-year construction period to build in Archer City. Texas Grace filed the subject Application for Review on January 16, 2001. On January 23, 2001 Texas Grace filed an "Emergency Motion for Stay."

4. On March 5, 2001, while the Application for Review and Stay Request were pending, the staff issued a letter at Texas Grace's request concerning the status of the Archer City permit. The staff letter states:

Should the Commission grant review, the Commission's *Order* will specify a new construction deadline. In the event that the Commission denies review, Texas Grace will have 79 days to complete construction and file a covering license application, commencing on the date such an *Order* is released.

The 79-day period is equal to the period of time between November 20, 2000, the date on which Texas Grace filed its Petition for Reconsideration, and the February 7, 2001 construction permit expiration. This suggests that the staff believed that the filing of the petition for reconsideration and pendency of the Application for Review of the denial of Texas Grace's tolling request would qualify as "encumbrances," and therefore would toll the running of the KRZB(FM) construction period.

5. Discussion. The Commission will grant an application for review only if the applicant demonstrates that the staff's decision: (1) conflicts with statute, regulation, case precedent, or established Commission policy; (2) involves a question of law or policy that has not been previously resolved by the Commission; (3) involves precedent or policy that should be overturned or revised; (4) makes an erroneous finding as to an important or material question of fact; or (5) commits a prejudicial procedural error. 47 C.F.R. § 1.115(b)(2)(i)-(v). Texas Grace's application for review consists of many allegations that focus on three core issues. First, Texas Grace contends that the staff erred in failing to treat the Archer City construction permit as an original construction permit for a "new" station that would be entitled to a new three-year construction period. Next, Texas Grace claims the staff erred in finding that its permit was not encumbered by administrative review. Finally, Texas Grace raises for the first time an allegation that the

(Continued from previous page)

73.202(b), *Table of Allotments, FM Broadcast Stations (Tipton, Mangu, Eldorado and Granite, Oklahoma, and Archer City, Texas)*, MM Docket No. 99-23, 14 FCC Rcd 21161 (1999) ("*Oklahoma R&O*").

staff's action conflicts with a staff waiver of the construction rules for unbuilt station KLTR(FM), Caldwell, Texas.³

6. The staff correctly rejected Texas Grace's claim that it is entitled to a new three-year construction period, to begin on February 7, 2000.⁴ On that date, the Mass Media Bureau modified the Olney permit to change the community of license to Archer City. Texas Grace is simply mistaken in its view that the staff's October 1997 issuance of a Notice of Proposed Rulemaking, *proposing* at Texas Grace's request to amend the FM Table of Allotments to specify Archer City instead of Olney, in some fashion cancelled or terminated the outstanding Olney permit. It is further mistaken in asserting that the staff's subsequent modification of the Olney construction permit to specify Archer City is treated under the Commission's rules as a new "original" construction permit.⁵

7. Community of license changes are modifications of outstanding authorizations. *See* 47 C.F.R. § 1.420(i) (permit's community of license may be modified in a rulemaking proceeding if the amended allotment would be mutually exclusive with the present assignment). Pursuant to the rules governing such changes, the staff properly considered Texas Grace's request to change KRZB's community of license as a modification of the station's existing permit, and not as a new original permit. *Significantly*, Texas Grace's August 7, 1997 rulemaking petition properly requested "that the construction permit of KRZB be modified to specify Archer City, Texas, as the station's community of license" (emphasis added). In response, the Commission issued a rulemaking proposal and a final order, both of which refer to this matter as a modification. In filing its application to implement this rulemaking, Texas Grace submitted the appropriate fee (\$725) for an application to modify an existing permit, not the fee (\$2600) for a new construction permit. Further, in providing required responses on the application form about the purpose of the application, Texas Grace correctly described the application as a "modification" of the outstanding Olney permit, file number BPH-960201MB, rather than as a "new station."⁶ Finally, the Archer City permit itself, file number BMPH-19990217IB, carries a modified FM station construction permit prefix, "BMPH", in which the "M" is an abbreviation for "modified" under the Commission's broadcast application numbering system.

8. Texas Grace maintains that the *Archer City Notice* issued in October 1997 rendered its Olney permit "no longer relevant or viable" because the Commission "noticed deletion of this Permit,

³ We have considered Texas Grace's allegations about the staff's handling of the December 14, 2000 letter, have read that letter, and find those allegations unsupported. Texas Grace has also complained that it has not been given due process in the treatment of its pleadings and arguments. We have considered these arguments and find them without merit. Texas Grace was entitled to seek Commission level review of the staff's decision. We have fully considered the application for review and amendments in a manner consistent with our statute and regulations. We find no basis for further review of these issues.

⁴ Texas Grace based its three-year claim, in part, on allegedly having received staff advice to that effect prior to issuance of the Archer City permit. While we would regret any erroneous advice that may have been given, it is well established that a permittee may not rely on informal advice from staff. *See Texas Media Group, Inc.*, 5 FCC Rcd 2851, 2852 (1990), *aff'd sub. nom. Malkan FM Associates v. FCC*, 935 F.2d 1313 (D.C. Cir. 1991).

⁵ *See* 47 C.F.R. § 73.3598(a) (original FM construction permits shall specify a construction "period of three years from the date of issuance of the original construction permit").

⁶ *See* Application, Section I, Section V-B, and Exhibit 2. *See also* Section V-B and Exhibits 3-4 of Texas Grace's June 22, 1999 amendment.

stating that the public interest would better be served if KRZB instead provided service at the new community of Archer City. . .” *Application for Review* at 3, 6. Texas Grace’s argument is erroneous. As a threshold matter, it was Texas Grace that filed a petition for rulemaking and requested the reallocation of its channel to Archer City and modification of its permit to specify Archer City; nothing compelled it to seek that reallocation and modification. Furthermore, even after it initiated the rulemaking proceeding, nothing prevented it from constructing its station at Olney. In this connection, the *Archer City Notice* did not find that “the public interest would better be served if KRZB instead provided service at the new community of Archer City,” as Texas Grace asserts; it simply stated that “petitioner’s proposal warrants consideration” and sought comment on that proposal. *Archer City Notice*, 12 FCC Rcd at 17513. That Notice did not delete the Olney channel or otherwise invalidate Texas Grace’s permit, as Texas Grace contends. Nor did the Report and Order in that proceeding impair Texas Grace’s authority to construct its station at Olney.⁷ Texas Grace had valid continuing authority to construct its station in Olney until February 7, 2000, when the staff, at Texas Grace’s request, modified the permit to specify Archer City as the community of license.⁸

9. We recognize, of course, that Texas Grace filed the Archer City petition for rulemaking because it preferred to construct a station that would serve this community. When the Commission decided in the *Streamlining R&O* to expand the radio station construction period from 18 to 36 months, it also eliminated former Section 73.3535(d) and its former practice of providing additional time for construction after a permit has been modified. *Streamlining R&O*, 13 FCC Rcd at 23090 (“in light of these new procedures, we eliminate the current practice of providing additional time for construction after a permit has been modified or assigned.”). On reconsideration, the Commission was specifically requested to expand tolling during “the pendency of petitions for rule making affecting a station’s frequency and/or class” and “modification applications.” *Streamlining MO&O*, 14 FCC Rcd at 17538-39. We denied those petitions. In so doing, it was our intent to limit tolling to those circumstances explicitly mentioned in the *Streamlining* decisions or in our rules. See 47 C.F.R. § 73.3598. Thus, a construction deadline would not be extended when, as here, the Commission modifies a station’s original permit at the station’s request or when the applicant otherwise voluntarily participates in a rulemaking proceeding.⁹ This policy is designed

⁷ The *Archer City R&O* conditioned modification of Texas Grace’s permit on submission of a minor change application and the filing of any required environmental assessment for the new transmitter site. See *Archer City R&O*, 13 FCC Rcd at 18922. Until the application was submitted and granted, Texas Grace continued to have authority to construct its station at Olney.

⁸ In a July 27, 2001 supplemental submission, Texas Grace seeks to clarify its arguments concerning the starting date of its three-year period. Texas Grace maintains that it had no authority to construct any station on February 16, 1999, a date used to determine a permittee’s eligibility to avail itself of the three-year provisions of the *Streamlining MO&O*. It asserts that it did not apply for an Archer City permit until the following day, February 17, 1999, and that the community of Olney was deleted from the table of allotments, effective November 17, 1998. Accordingly, Texas Grace believes that its three year construction period could not start, at the earliest, until the grant of the Archer City permit. This view is incorrect. On February 16, 1999, Texas Grace held a valid permit for Olney and thus was entitled, pursuant to the *Streamlining MO&O*, to an expiration date no earlier than December 21, 2000. *Streamlining MO&O*, 14 FCC Rcd at 17536. Texas Grace received what it was entitled to because its permit, as modified, did not expire until February 7, 2001.

⁹ Texas Grace initiated the rulemaking proceeding in Docket No. 97-225, concerning the Olney and Archer City allotments, and other parties filed counterproposals. Texas Grace maintains that rulemaking proposals by others drew it into subsequent Archer City rulemaking proceedings involuntarily. With respect to Docket No. 99-23, the record indicates that the party initiating that proceeding proposed changes only to allotments in Oklahoma. (continued....)

to encourage prompt construction and to discourage permittees from using the permit modification process to warehouse spectrum. *Streamlining R&O*, 13 FCC Rcd at 23093. It is also a policy designed to promote prompt introduction of service to the public by clearly placing on each permittee's shoulders the burden of completing construction by a certain date. Indeed, our action in the *Streamlining Order* doubling the construction period for a new radio station reflected a specific balancing of our interest in expeditious construction and avoiding waste of Commission and applicant resources on an endless variety of requests to extend the authorized construction period. See *Streamlining MO&O*, 14 FCC Rcd at 17533, 17539. The substantial additional time afforded by the new construction period was in large part intended to permit applicants enough time to resolve local land use issues and to make whatever reasonable changes in its permit or proposed facilities were necessary, and still be able to construct the station without seeking extensions from the Commission. *Id.* at 17539-17541. Accordingly, the staff acted consistently with our intent when it included the period during which the Olney construction permit was outstanding and unencumbered (October 7, 1996 through February 7, 2000) in calculating the construction deadline for the Archer City facility.

10. Unfortunately, in the course of the present proceeding, we have come to realize that our intent may not have been completely clear to permittees with then-outstanding modification requests stemming from rulemaking proceedings. Specifically, while noting our receipt of requests to expand our tolling provisions to recognize modifications and rulemaking requests, we denied those requests without discussion. See *Streamlining MO&O*, 14 FCC Rcd at 17538. A permittee, like Texas Grace, might have concluded that reliance on mere facilities modifications involving frequency or class would be insufficient to trigger tolling, but that a facility change coupled with a community of license change might be treated differently. In view of this circumstance, we will waive our rules to provide Texas Grace with an additional three years to complete construction, commencing with the release date of this order. With respect to future cases, however, we emphasize that only the circumstances explicitly identified in Section 73.3598(b) of our rules and in our *Streamlining* decisions will toll a permit. These circumstances are limited to the following: (1) construction is prevented due to an act of God defined in terms of natural disasters (Section 73.3598(b)(i)); (2) the grant of the permit is the subject of administrative or judicial review (Section 73.3598(b)(ii)); (3) there is failure of a Commission-imposed condition precedent to

(Continued from previous page)

See *Oklahoma R&O*, n. 2 *supra*. The Oklahoma proposals were fully spaced to the town center of Archer City, Texas but Texas Grace believed that they would not provide full spacing to Texas Grace's preferred Archer City site. Rather than filing opposing comments, or a counterproposal limited to Oklahoma allotments, Texas Grace filed a counterproposal that would upgrade the Archer City, Texas allotment. Absent Texas Grace's counterproposal, changes to the Archer City allotment would never have been at issue. With respect to the remaining proceeding, Docket No. 00-148, Texas Grace reports that a party filing a counterproposal in that proceeding proposed to modify the channel of the Archer City allotment. No decision on that proposal has yet been reached. See *Notice of Proposed Rulemaking*, MM Docket No. 00-148 (Quanah, Texas), 15 FCC Rcd 15809 (2000). We note that the mere pendency of a rulemaking proposal does not encumber a permittee's ability to construct pursuant to its existing authorization. Further, these circumstances pose no financial risk to the permittee who constructs during such a proceeding. Whenever an existing licensee or permittee is ordered to change frequencies involuntarily to accommodate a new channel allotment, longstanding Commission policy requires the benefiting party or parties to reimburse the affected station for costs incurred. See *Circleville, Ohio*, 8 FCC 2d 159 (1967). Thus, we reject Texas Grace's tolling argument based on allegedly involuntary Archer City allotment changes. The proceedings in MM Dockets 97-225 and 99-23 were voluntary, and were resolved in Texas Grace's favor. The proceeding in Docket No. 99-148 remains ongoing and poses no financial risk to Texas Grace. We conclude that these proceedings have posed no impediment to the prompt construction of the authorized Archer City facilities.

commencement of operation (*Streamlining MO&O*, para. 39); or (4) there is one of the limited circumstances involving LPTV permittees discussed in paragraph 40 of the *Streamlining MO&O*. As we also have stated, we will entertain waiver requests if there are rare and exceptional circumstances beyond the permittee's control which would warrant the tolling of construction time (*Streamlining MO&O*, para. 42).

11. In the interest of thoroughness and to provide guidance to future permittees, we next consider Texas Grace's argument that the staff erred in denying its tolling request. As noted above, the Commission tolls a station's three-year construction period when the permittee notifies the staff, pursuant to 47 C.F.R. § 73.3598(c), that construction has been encumbered by administrative or judicial review of a grant of a construction permit; by judicial review of any cause of action relating to necessary local, state or federal requirements for the construction and/or operation of the station; and/or by an "act of God" (*i.e.*, weather related disasters such as tornadoes, hurricanes, floods, and earthquakes). *Streamlining R&O*, 13 FCC Rcd at 23091. Permit expiration also would be tolled if a party promptly builds but cannot commence operations as required, due to a failure of a Commission-imposed condition precedent. *Streamlining MO&O*, 14 FCC Rcd at 17540. Upon resolution of the *bona fide* tolling event, we allow the permittee to recoup the time during which its permit was encumbered, adjusting the expiration date of the permit so that the permittee will receive a full unencumbered three years to construct.

12. Texas Grace alleges that the staff erroneously ignored certain events that Texas Grace contends would constitute "administrative review" within our tolling rules. According to Texas Grace, the staff characterized its tolling request as relying merely on Texas Grace's own rulemaking requests, but erroneously ignored other staff "review" functions including the "consideration" of counterproposals, issuance of notices of proposed rulemaking, amendment of the table of allotments, "consideration" of Texas Grace's application to implement the change in community of license, and ongoing "consideration" of a rulemaking proposal from another party that has the potential to modify Texas Grace's assigned channel from 248C2 to 230C1. Texas Grace maintains that tolling is warranted because these staff actions "obstructed KRZB's ability to construct its pending Archer City broadcast station." Texas Grace also claims that the staff ignored its argument that its permit was tolled for purposes of administrative review during the pendency of its initial tolling request.

13. We do not find these arguments persuasive. The staff's December 2000 action thoroughly discussed all aspects of Texas Grace's tolling request, specifically identifying and summarizing seven of its arguments. These included Texas Grace's claims of rulemaking as administrative review, health-related problems as "acts of God," and the staff's consideration of its initial tolling request as administrative review. The staff correctly found that neither the rulemaking nor any of the other matters cited by Texas Grace constitute "administrative review" under the new construction period requirements. For tolling purposes, our rules define administrative review as consideration of "petitions for reconsideration and applications for review of the grant of a construction permit." 47 C.F.R. § 73.3598(b)(ii). It is not triggered, as Texas Grace argues, by every action that may need staff approval. Therefore, we find that Texas Grace's arguments were thoroughly considered and properly resolved by the staff, and we uphold the staff's decision for the reasons stated therein. *See e.g.*, *WAMC, Inc.*, 10 FCC Rcd 12219 (1995) (denying application for review raising essentially the same arguments as in petition for reconsideration).

14. Finally, Texas Grace now raises two additional arguments for the first time. It maintains that the denial of its tolling request is inconsistent with the treatment afforded a Caldwell, Texas permittee. It also indicates that it is having difficulty obtaining financing to build the station because its bank has advised that "the shortchanged construction time would pose an unacceptable risk to justify the loan." The Commission's rules provide that "no application for review will be granted if it relies on questions of fact

or law upon which the designated authority has been afforded no opportunity to pass.” See 47 C.F.R. § 1.115(c). Accordingly, we decline to address these issues. In any event, we note in passing that *Caldwell* involved a fundamentally different factual situation¹⁰ and that a permittee’s financial difficulties are not grounds for tolling.¹¹ Accordingly, we deny Texas Grace’s Application for Review and affirm the staff’s decision.

15. Although we affirm the staff’s December 14, 2000 decision, which properly denied tolling, we take this opportunity to correct certain staff errors during the course of this proceeding, which resulted in extending the deadline by which Texas Grace must complete construction. As a preliminary matter, the staff’s designation of February 7, 2001 (one year from grant of modification) as the expiration date of Texas Grace’s permit was in error. The *Streamlining R&O*, 13 FCC Rcd at 23090, eliminated the former practice of giving additional time for permit modifications. Texas Grace’s Archer City permit should have specified, pursuant to *Streamlining MO&O*, 14 FCC Rcd at 17536, December 21, 2000 as the correct expiration date. That is the final date to which we extended all valid outstanding broadcast permits that otherwise would have expired previously.

16. The staff also erred in its March 5, 2001 status letter advising Texas Grace that it would receive an additional 79-day period for construction if review is denied. That calculation erroneously assumes that the Commission should treat the pendency of Texas Grace’s Petition for Reconsideration and its Application for Review as qualifying “administrative review” tolling events. Those two pleadings, however, were filed in response to the staff’s denial of tolling, whereas we restrict “administrative review” to petitions for reconsideration and applications for review which challenge grants of construction permits or of permit extensions, and judicial appeals of Commission action concerning such grants. Thus, if the staff grants an initial permit or a tolling request and another party seeks review of that grant, we do not require a permittee to build pursuant to a grant that is not final and subject to challenge. In contrast, a permittee’s unilateral request for review of a denial of a request for additional time to construct, as in the present case, does not raise similar issues and does not fall within the scope of “administrative review” for tolling purposes.¹² 47 C.F.R. § 73.3598(b)(ii). *Streamlining R&O*, 13 FCC Rcd at 23091.¹³

¹⁰ In *Caldwell*, the staff concluded that allocations rulemaking proceedings and related matters generally do not qualify for tolling, but waived the construction rule based on its finding that the lengthy agency and court review of an involuntary channel change in that case created unique circumstances analogous to the administrative and judicial review of the grant of a construction permit. *Letter to Robert J. Buenzle, Esq. from Linda Blair, Chief, Audio Services Division* (October 31, 2000) (“*Caldwell*”). Unlike *Caldwell*, there has been no review of any of the Archer City rulemaking proceedings, nor are the circumstances here analogous at all to that case. See also note 9 *supra*.

¹¹ To the extent that Texas Grace argues that the staff’s actions made it difficult for it to obtain financing, we note that Texas Grace certified when it first applied for its permit that sufficient liquid assets were on hand or that sufficient funds were available from committed sources to construct the proposed facility and to operate it for three months without revenue. See *Application BPH-19960201MB*, Section III, Financial Qualifications. See also, *Merrimack Valley Broadcasting, Inc.*, 82 FCC 2d 166, 167 (1980). Cf. *Instructions for FCC Form 301, General Instruction K* (May 1999) (application form in use today, which no longer contains a financial certification, continues to require reasonable assurance of committed financing sufficient to construct and operate without revenue for three months).

¹² We note that Texas Grace makes a related, but expanded, argument in its Application for Review. Just as we find the staff was mistaken in treating Texas Grace’s filing of its Petition for Reconsideration on November 20, (continued...)

17. In sum, we conclude above that Texas Grace has no right to additional time to construct its station under our current rules, as modified in the *Streamlining* proceeding. Nevertheless, due to a possible previous lack of clarity in our policy with respect to changes of communities of license, we will waive our rules on our own motion so as to extend the expiration date of Texas Grace's construction permit to three years from the release date of this order. We deny Texas Grace's emergency stay request to toll the construction period during administrative review of its Application for Review and judicial review of this order. We also deny the request for a stay pending any administrative or judicial review. For the reasons set forth above, the staff's rejection of Texas Grace's arguments fully accorded with our rules, and it is thus unlikely to prevail on the merits of any appeal. See *Virginia Ass'n v. FCC*, 259 F.2d 921 (D.C. Cir. 1958), modified, *Washington Metropolitan Transit Authority v. Holiday Tours*, 559 F.2d 841 (D.C. Cir. 1977). Further, there is no evidence of irreparable injury here, as Texas Grace may well complete construction prior to the expiration of the permit, which has been substantially extended by waiver herein. *Id.* Indeed, since Texas Grace is being granted more time to construct than it would be entitled to without a rule waiver, it has suffered no injury at all.

18. Accordingly, IT IS ORDERED that the Application for Review filed by Texas Grace Communications IS DENIED and that its Motion for Stay IS DENIED. On our own motion, 47 C.F.R. Section 73.3598(a) IS WAIVED to provide that the construction permit for station KRZB(FM) will expire three years from the release date of this order. Texas Grace must complete construction by that date and timely file an application for a license to cover the authorized facilities. Failure to file a timely license application will result in the automatic cancellation of the KRZB(FM) construction permit.

FEDERAL COMMUNICATIONS COMMISSION

Magalie Roman Salas
Secretary

(Continued from previous page) _____


2000 as initiating administrative review, we similarly reject Texas Grace's argument that it would qualify for tolling from October 20, 2000 (the date the staff denied its tolling request) continuing to the date on which any judicial appeal from this decision is resolved.

¹³ The treatment of the filing of the Petition for Reconsideration and Application for Review as tolling events was also erroneous for a second, independent reason. When Texas Grace filed its Petition for Reconsideration on November 20, 2000, it had already received an unencumbered construction period of four years, one month, and 13 days from the October 7, 1996 grant of KRZB's original permit, whereas the *Streamlining R&O*, in permitting the extension of then-outstanding construction permits to take advantage of the new three-year construction period and tolling procedures specifically noted that "[n]o additional time will be granted when the permittee has had, in all, at least three unencumbered years to construct." *Streamlining R&O*, 13 FCC Rcd at 23092. For these reasons, Texas Grace will not be eligible for a further extension of the construction deadline we provide by our action herein.

Attachment F

(Channel Study for Channel 248A at Chillicothe, Texas)


FM PROSP^(TM) LOCATE STUDY CH 248 A 97.5 MHz

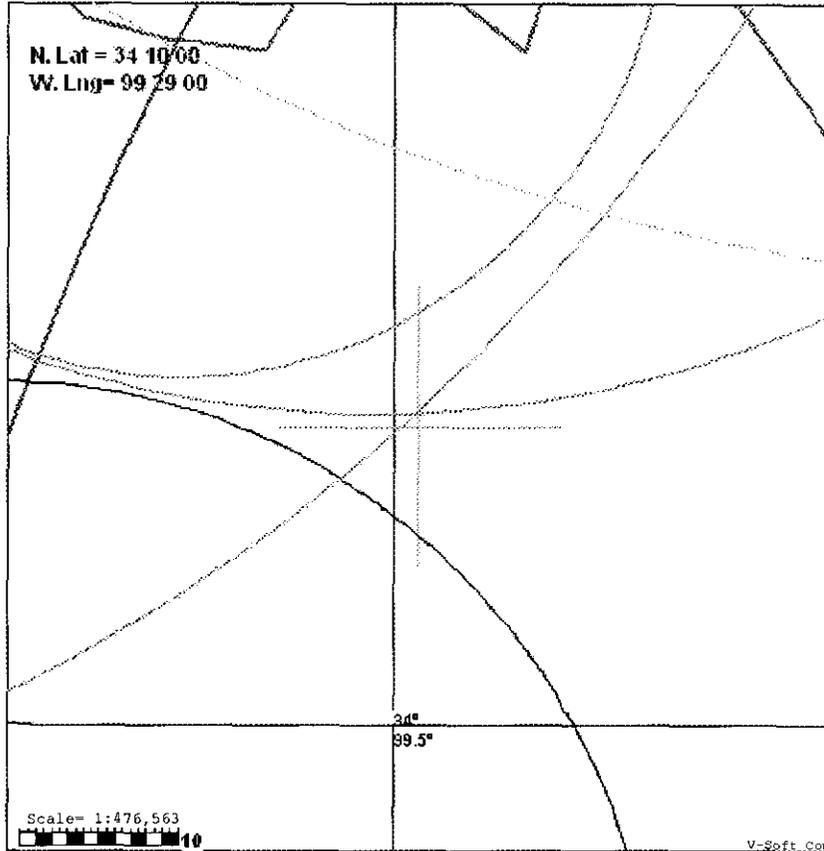

Dates:
 Data:12-07-04
 Job :12-12-04

Call	CH#	Type	Location		D-KM	Azi	FCC	Margin
RADD	248C1	ADD	Holliday	TX	76.05	141.1	200.0	-123.95
AL248	248C1	RSV	Archer City	TX	83.88	136.7	200.0	-116.12
RDEL	248C1	DEL	Archer City	TX	83.88	136.7	200.0	-116.12
KRZB.C	248C2	CP	Archer City	TX	84.29	113.6	166.0	-81.71
RDEL	248C2	DEL	Archer City	TX	84.29	113.6	166.0	-81.71
RADD	248C	ADD	Keller	TX	202.00	113.2	226.0	-24.00
RADD	248C	ADD	Keller	TX	202.00	113.2	226.0	-24.00
RDEL	248A	DEL	Wellington	TX	115.72	318.8	115.0	0.72
AL248	248A	VAC	Wellington	TX	115.72	318.8	115.0	0.72
KHIM	249A	LIC	Mangum	OK	72.84	357.8	72.0	0.84
RADD	250C3	ADD	Crowell	TX	47.35	214.1	42.0	5.35
AP245	245A	APP	Eldorado	OK	37.25	336.1	31.0	6.25
AL245	245A	VAC	Eldorado	OK	37.25	336.1	31.0	6.25
KWEYFM	247C1	LIC	Weatherford	OK	148.78	17.5	133.0	15.78
RDEL	247C1	DEL	Weatherford	OK	148.78	17.5	133.0	15.78

Chillicothe, TX CH 248A 70 dBu

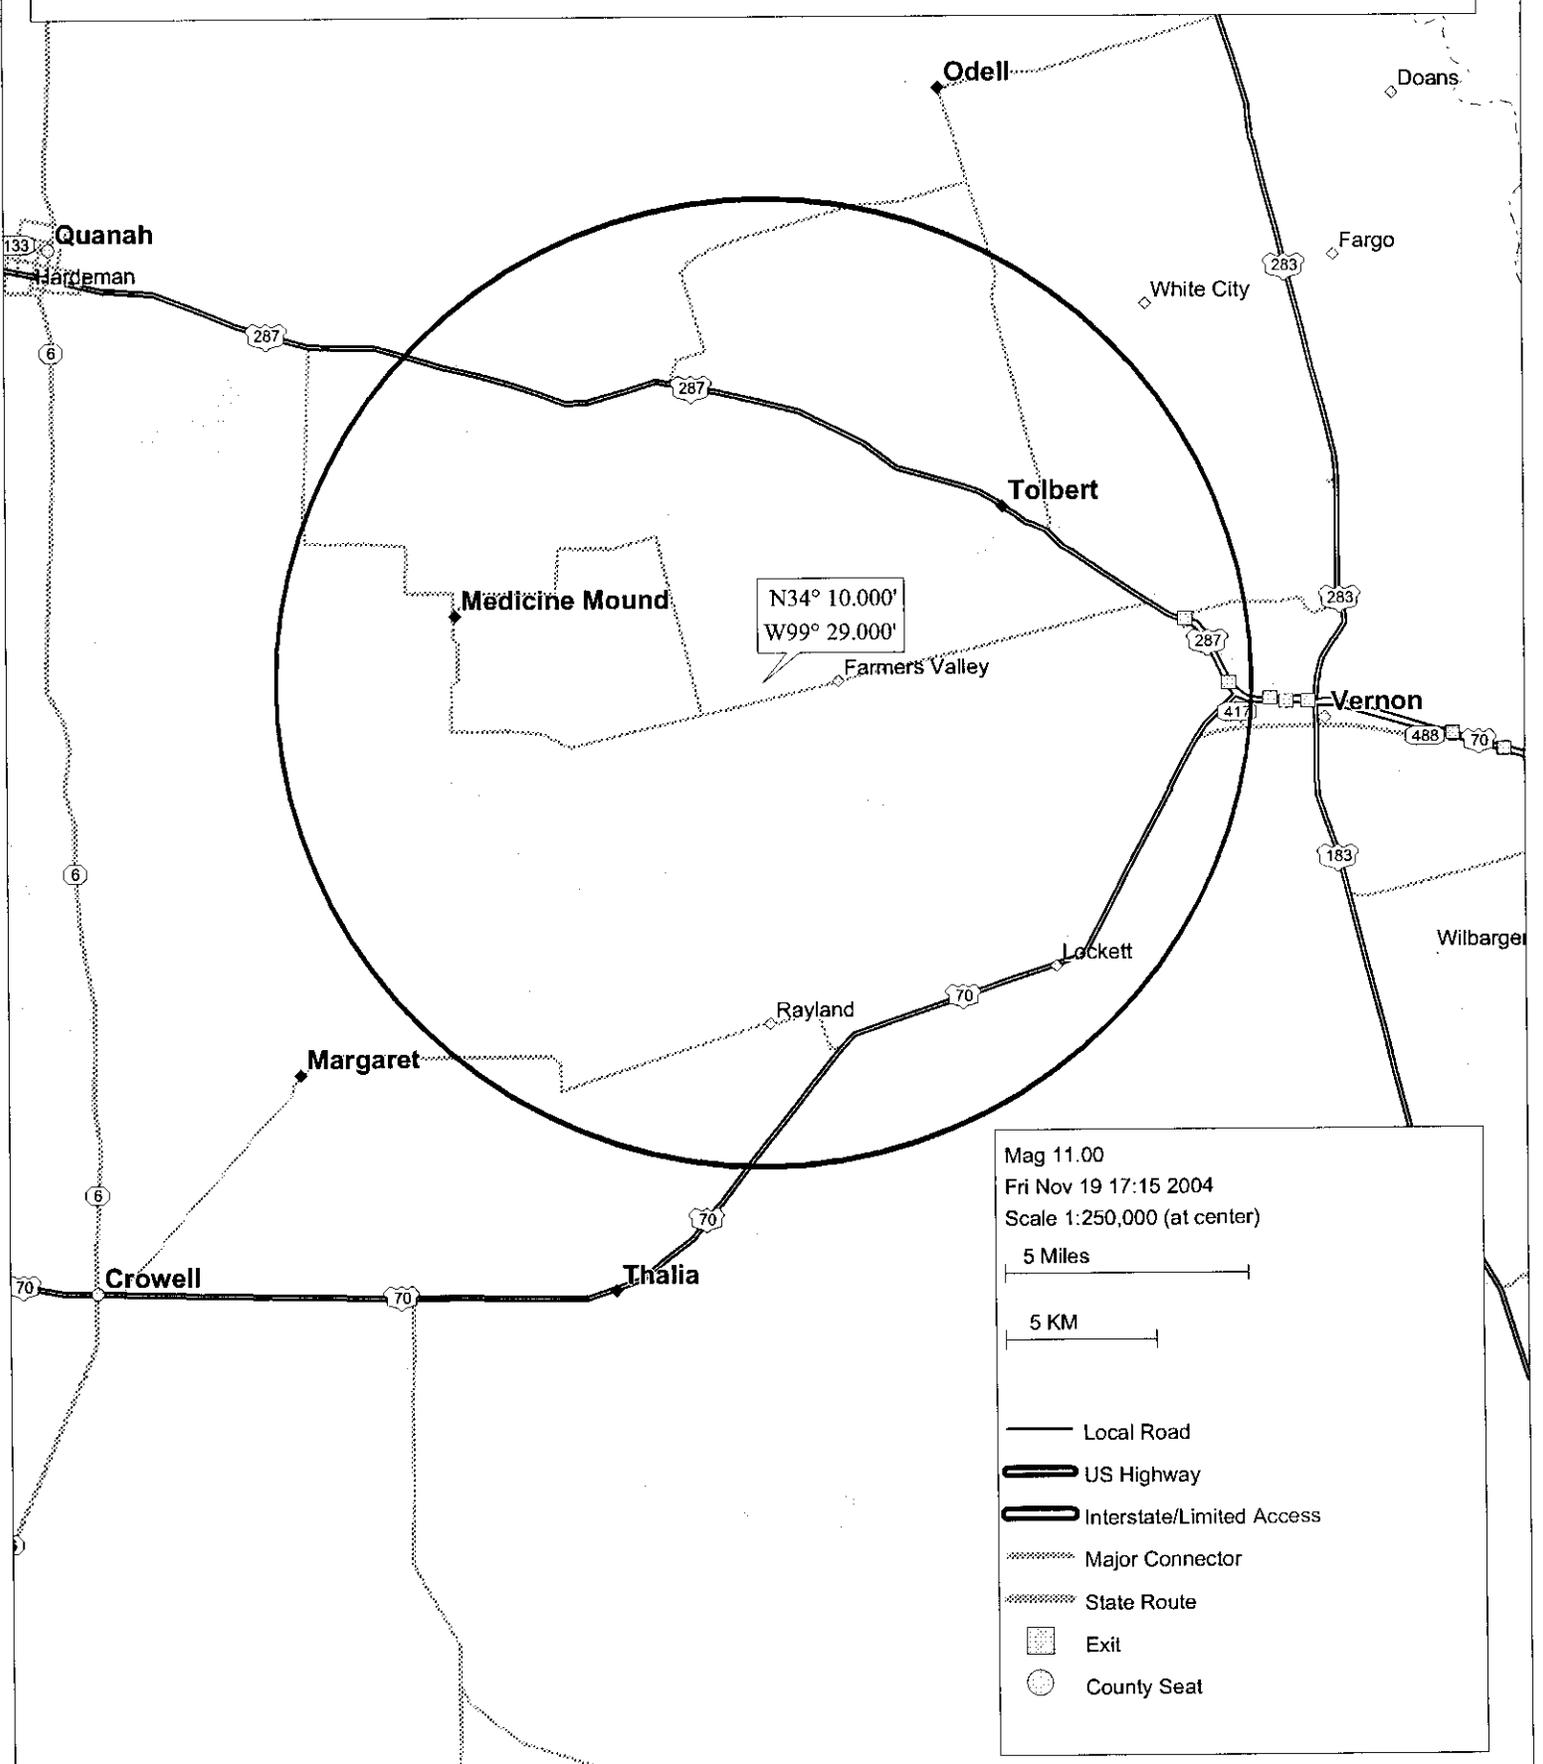


Mag 11.00
Fri Nov 19 17:15 2004
Scale 1:250,000 (at center)

5 Miles

5 KM

- Local Road
- US Highway
- Interstate/Limited Access
- Major Connector
- State Route
- Exit
- County Seat

Chillicothe, TX CH 248A 70 dBu

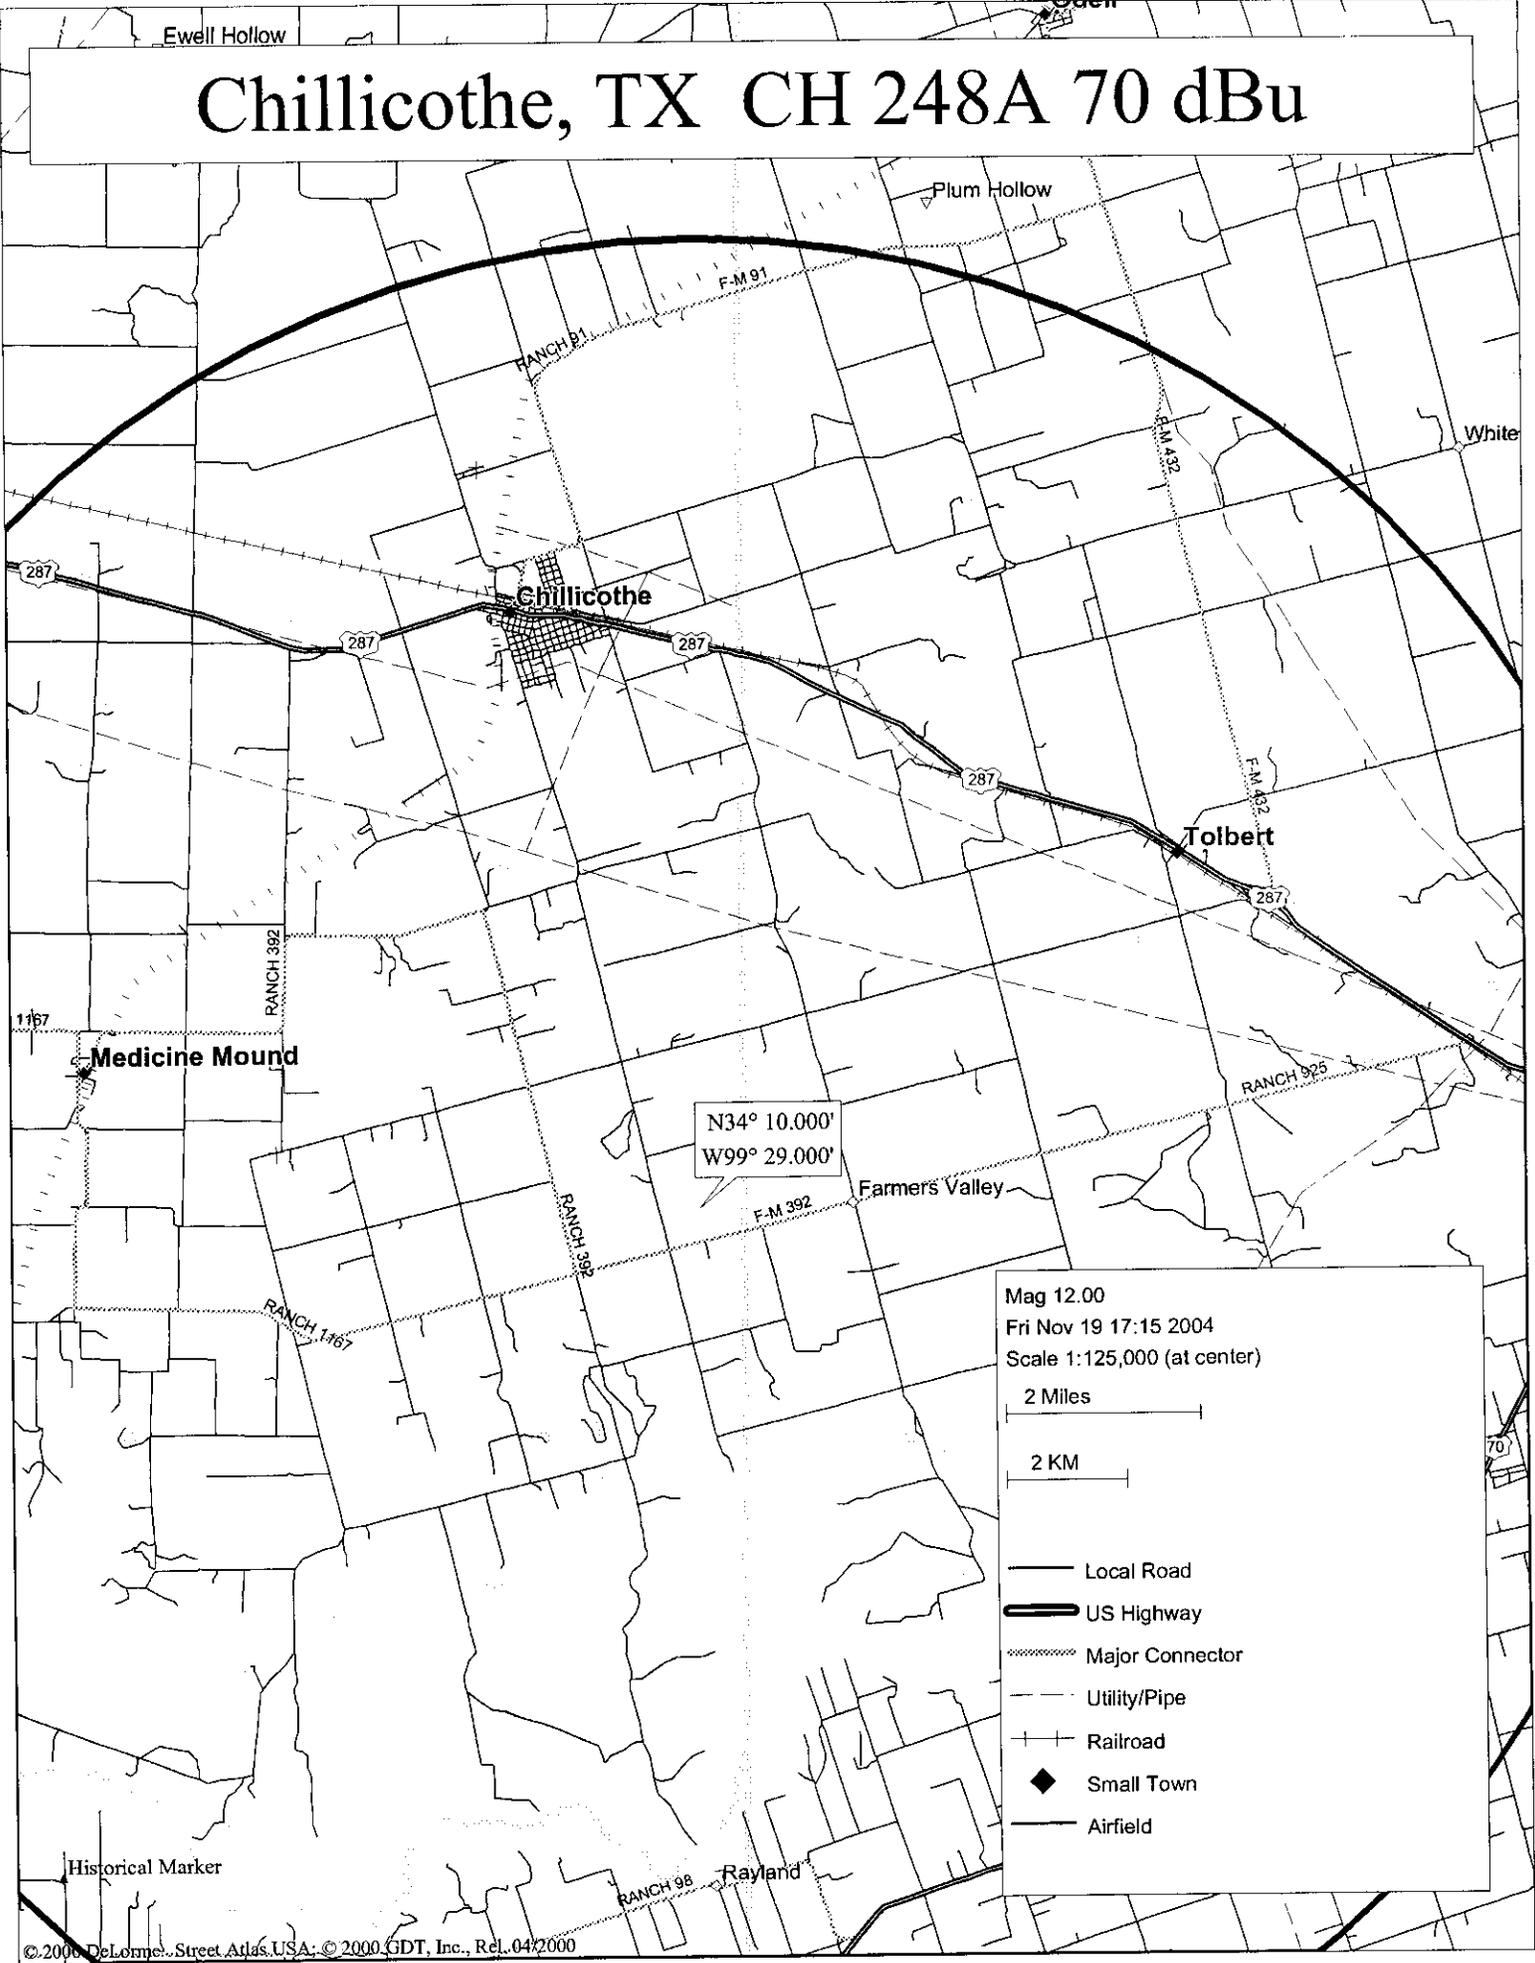

N34° 10.000'
W99° 29.000'

Mag 12.00
Fri Nov 19 17:15 2004
Scale 1:125,000 (at center)

2 Miles


2 KM

- Local Road
- US Highway
- Major Connector
- Utility/Pipe
- Railroad
- Small Town
- Airfield

Attachment G

(Channel Study for Channel 248A at Woodson, Texas)


FM PROSP^(TM)LOCATE STUDY CH 248 A 97.5 MHz

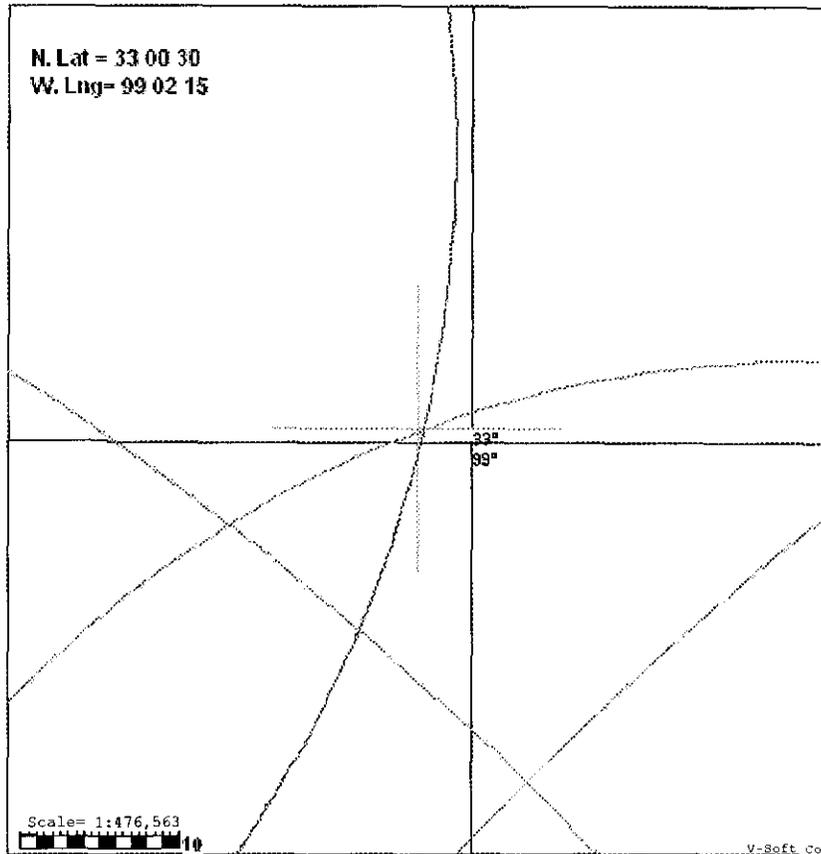


Dates:
 Data:12-07-04
 Job :12-12-04

Call	CH#	Type	Location		D-KM	Azi	FCC	Margin
RDEL	248C1	DEL	Archer City	TX	69.37	13.5	200.0	-130.63
AL248	248C1	RSV	Archer City	TX	69.37	13.5	200.0	-130.63
RADD	248C1	ADD	Holliday	TX	69.63	5.4	200.0	-130.37
RADD	248C	ADD	Keller	TX	152.35	71.3	226.0	-73.65
RADD	248C	ADD	Keller	TX	152.35	71.3	226.0	-73.65
KRZB.C	248C2	CP	Archer City	TX	101.29	20.8	166.0	-64.71
RDEL	248C2	DEL	Archer City	TX	101.29	20.8	166.0	-64.71
KVRPFM	246C1	LIC	Haskell	TX	74.62	283.4	75.0	-0.38
KATX.A	249A	APP	Eastland	TX	72.22	160.0	72.0	0.22
KATX	249A	LIC	Eastland	TX	72.22	160.0	72.0	0.22
KGKLFM	248C1	LIC	San Angelo	TX	212.00	218.0	200.0	12.00
KWTXFC	248C*	CP	Waco	TX	246.70	138.3	226.0	20.70
KWTXFM	248C	LIC	Waco	TX	246.71	138.4	226.0	20.71

Woodson, TX CH 248A 70 dBu

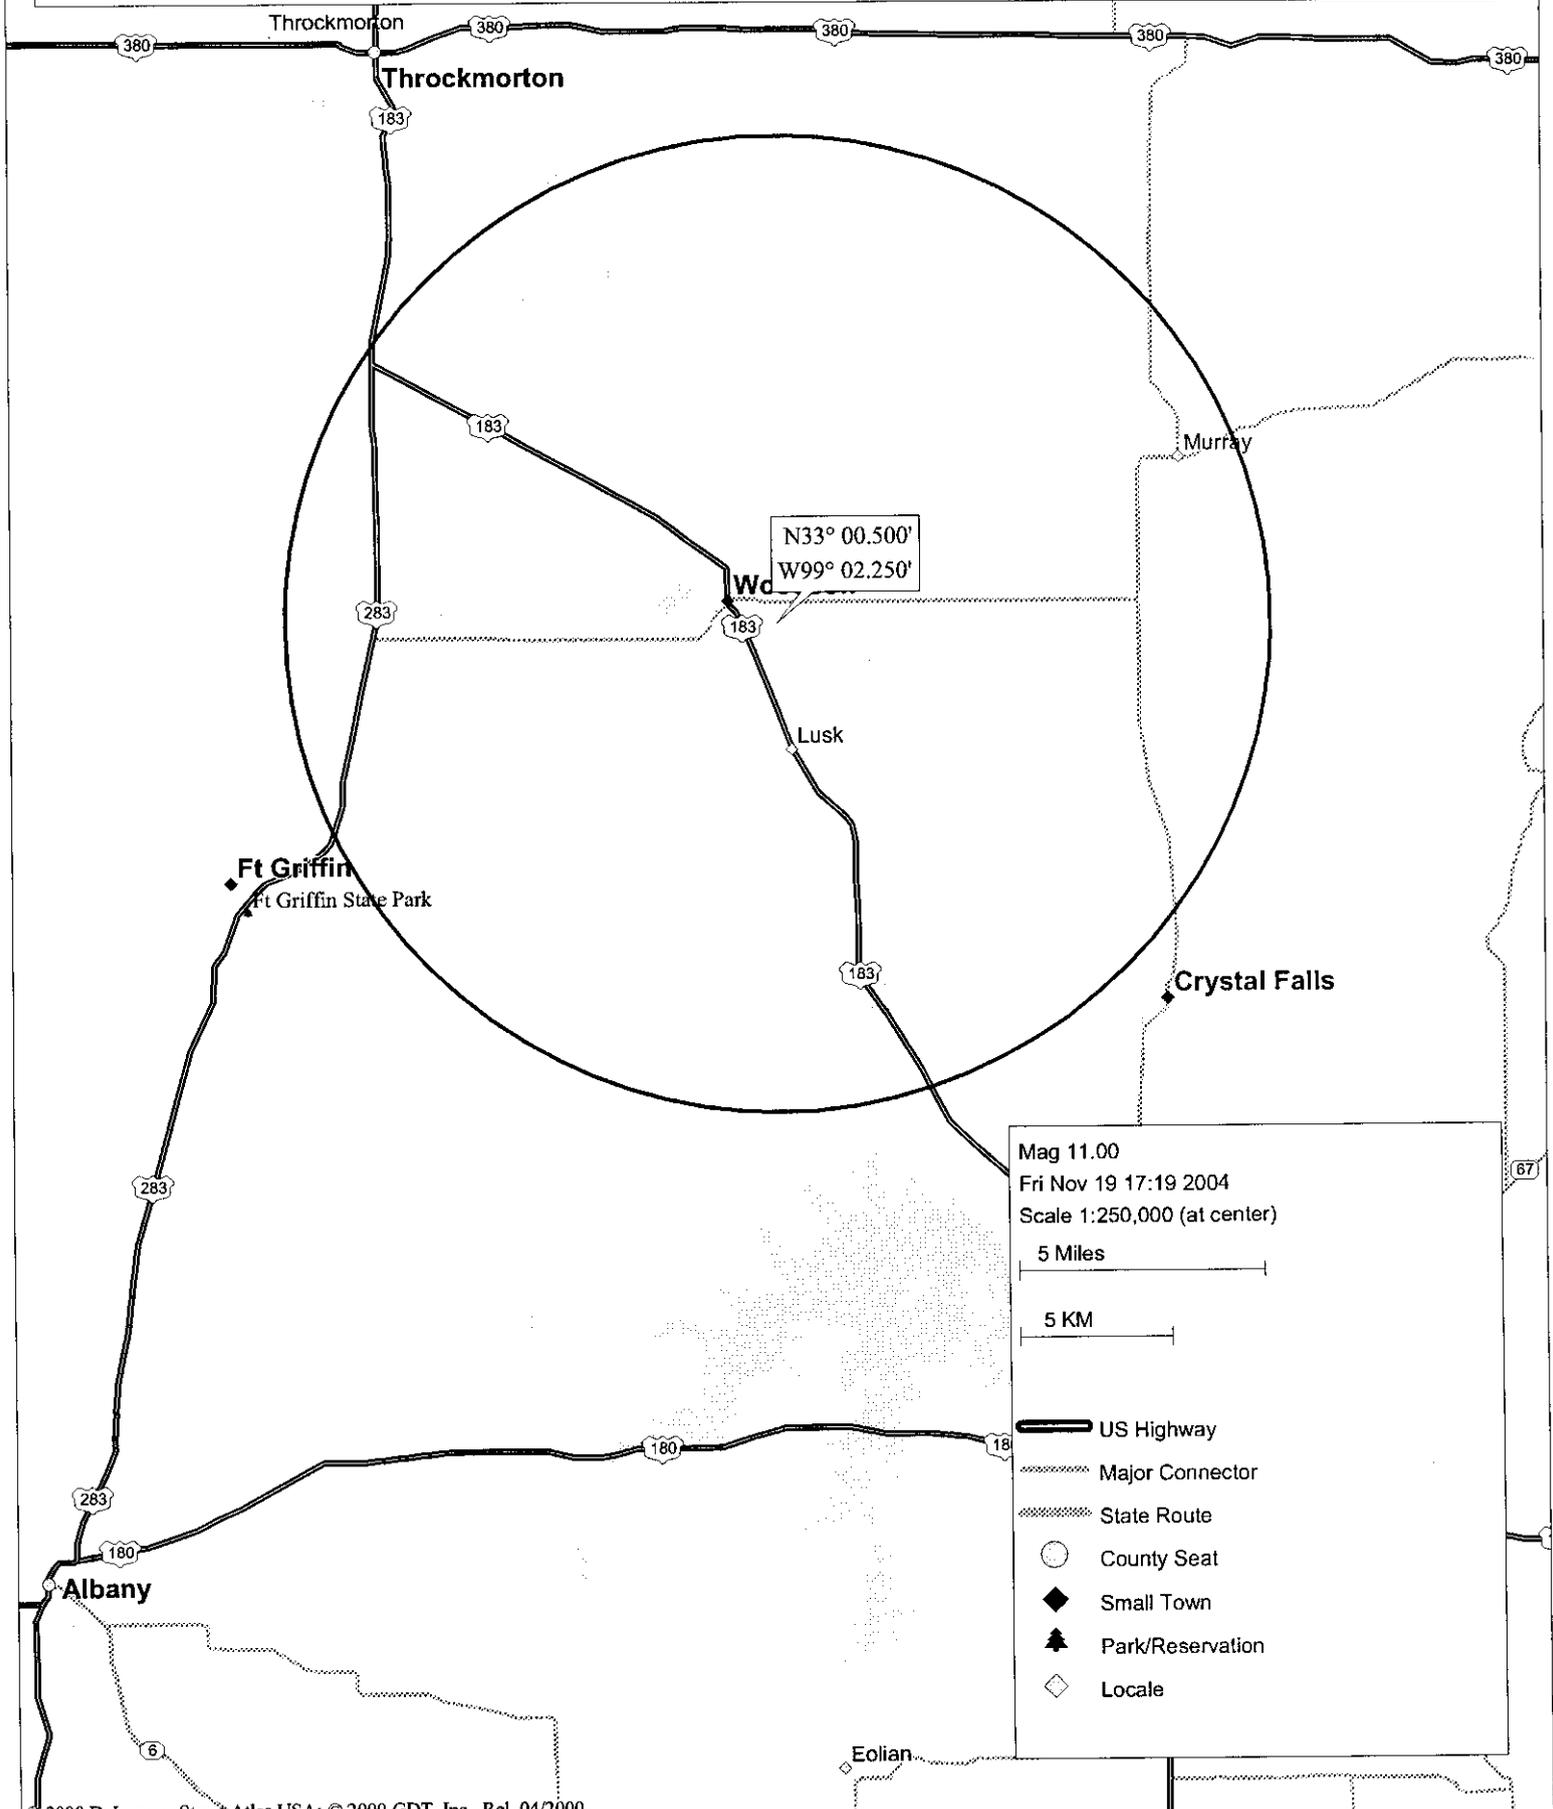

Mag 11.00
Fri Nov 19 17:19 2004
Scale 1:250,000 (at center)




- US Highway
- Major Connector
- State Route
- County Seat
- Small Town
- Park/Reservation
- Locale

Attachment H

(Channel Study for Channel 299C2 at Archer City, Texas)


FM PROSP^(TM) LOCATE STUDY CH 299 C2 107.7 MHz

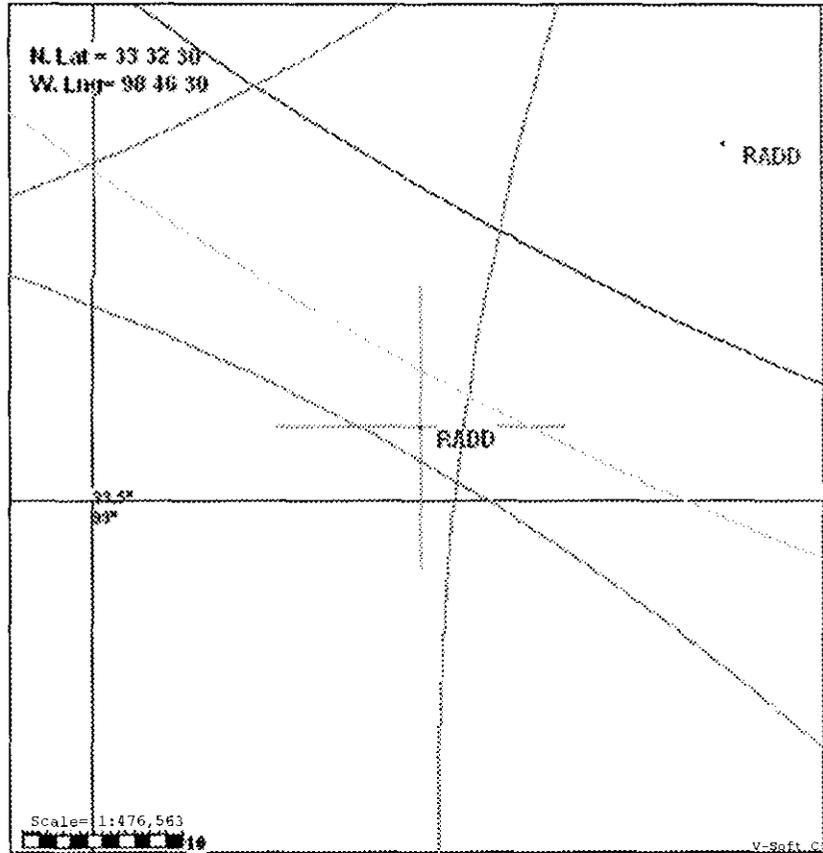

Dates:
 Data:12-07-04
 Job :12-12-04

Call	CH#	Type	Location		D-KM	Azi	FCC	Margin
RADD	299C2	ADD	Archer City	TX	0.00	0.0	190.0	-190.00
RADD	299C3	ADD	Holliday	TX	26.12	47.6	177.0	-150.88
RADD	298C2	ADD	Seymour	TX	48.96	275.2	130.0	-81.04
RADD	298A	ADD	Woodson	TX	63.96	203.9	106.0	-42.04
KEYJFM	300C1	LIC	Abilene	TX	159.87	208.7	158.0	1.87
KESSFM	300C1	LIC	Lewisville	TX	160.72	98.0	158.0	2.72
KRXO	299C*	LIC	Oklahoma City	OK	252.10	27.5	249.0	3.10
RDEL	299C	DEL	Oklahoma	OK	252.10	27.5	249.0	3.10
RADD	299C0	ADD	Oklahoma	OK	252.10	27.5	239.0	13.10
KEYB	300C2	LIC	Altus	OK	153.46	333.0	130.0	23.46

Archer City, TX CH 299C2 70 dBu

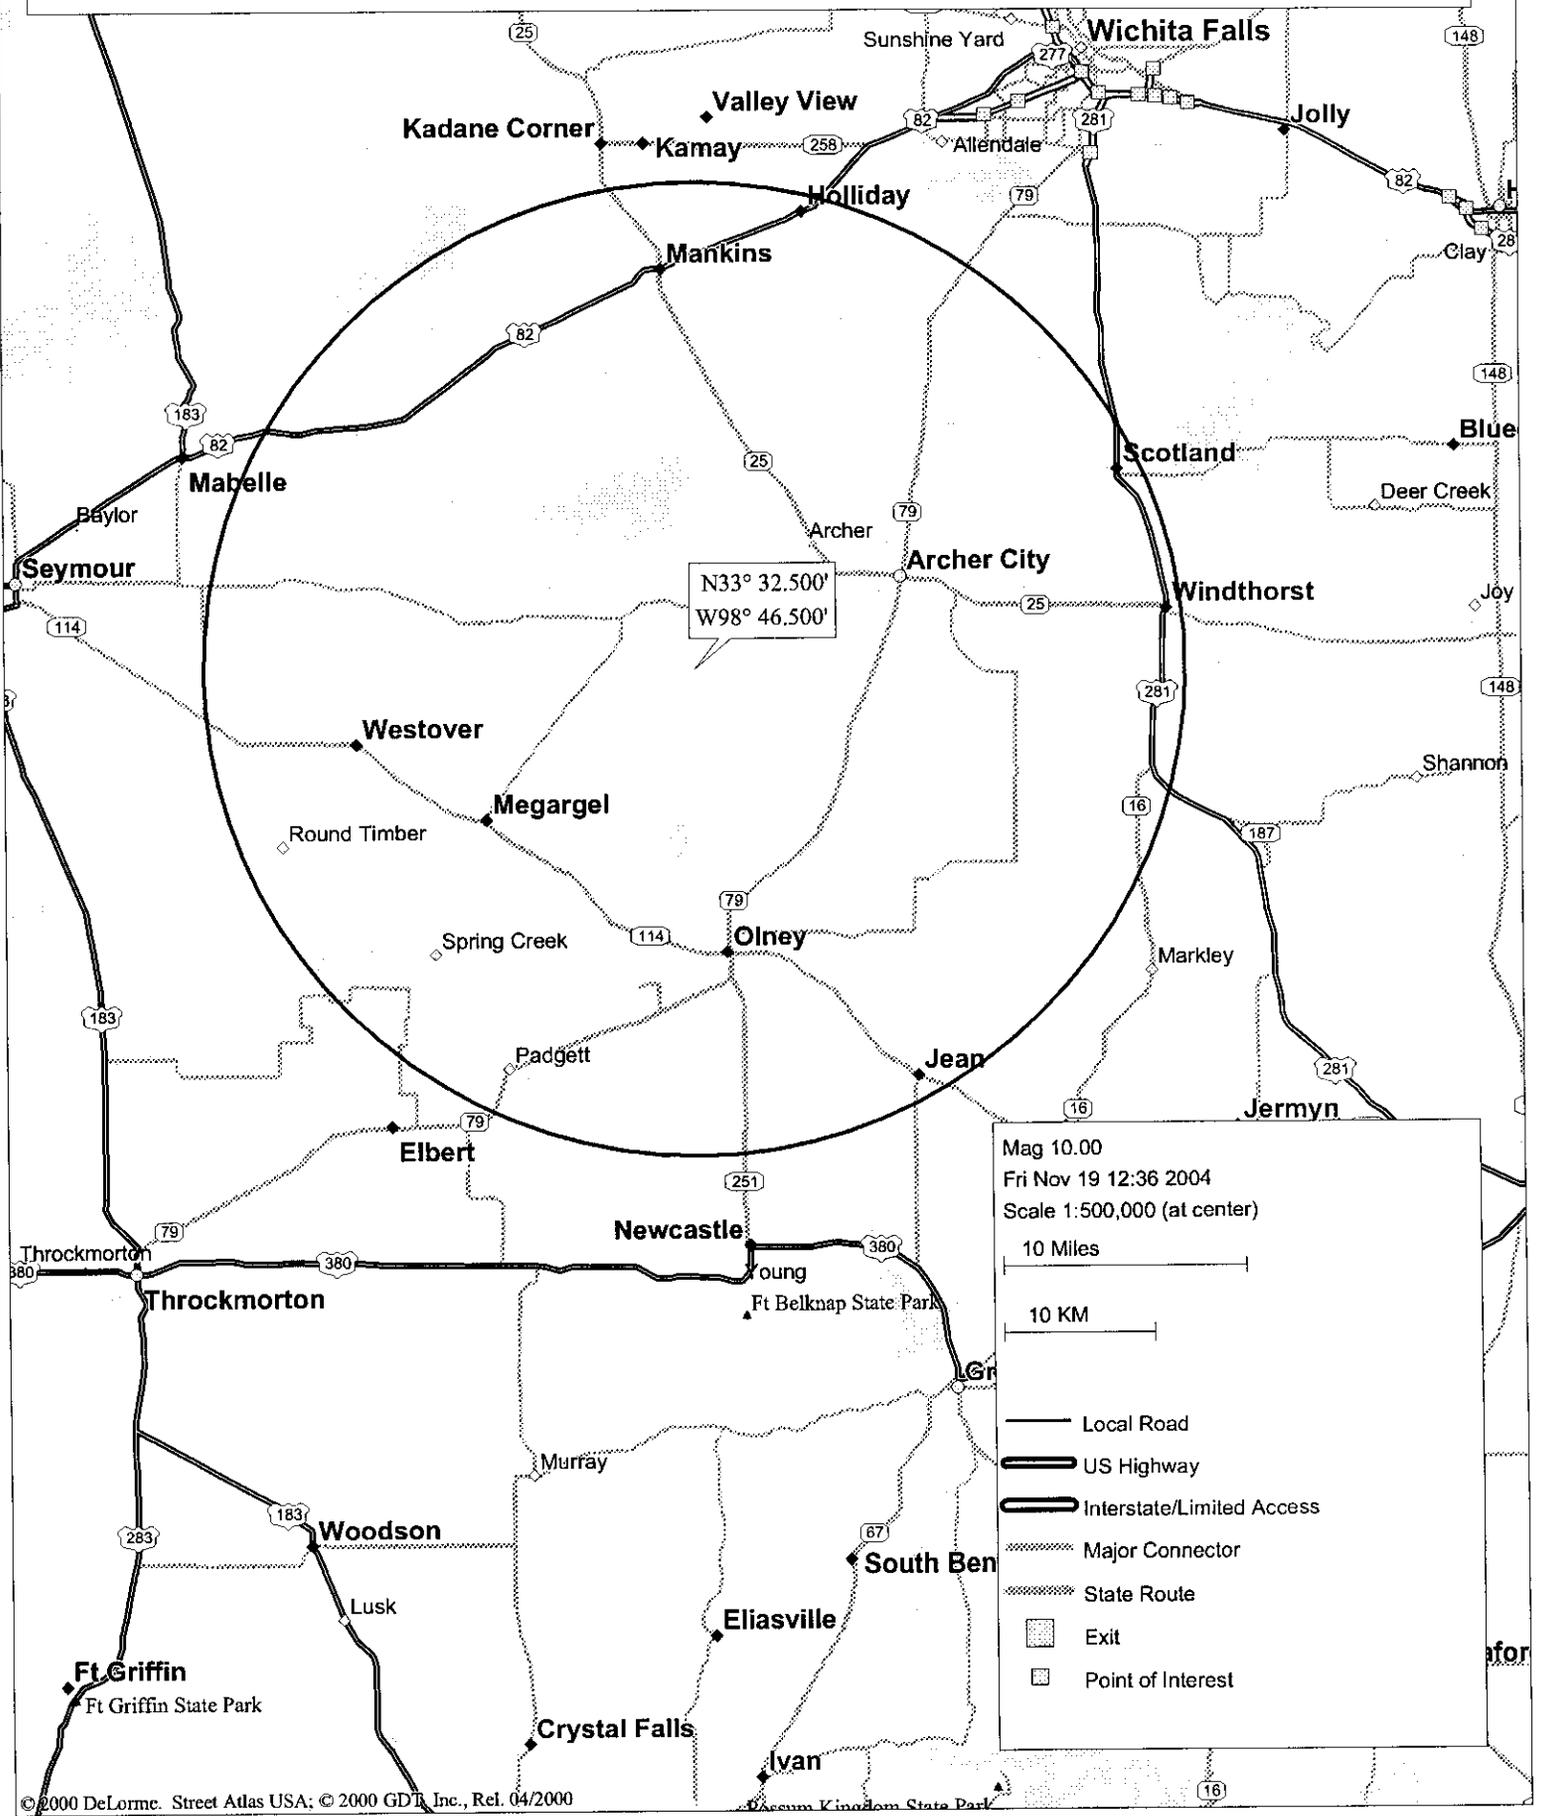

Attachment I

(FCC letter dated November 3, 2004, dismissing the petition to add Channel 299C3 at Holliday, Texas)



Federal Communications Commission
Washington, D.C. 20554

November 3, 2004

Mr. Charles Crawford
4553 Bordeaux Avenue
Dallas, Texas 75205

Dear Mr. Crawford:

This is in response to the petition for rule making you filed proposing the allotment of Channel 299C3 at Holliday, Texas, as the community's first local aural transmission service. On October 6, 2004, you filed a motion to dismiss your petition.

Since you are no longer interested in pursuing the allotment, as requested, we will dismiss your petition. In accordance with Section 1.420(j) of the Commission's Rules, you have provided the required affidavit certifying that you have not received, either directly or indirectly, any money or other consideration in connection with the dismissal.

Based on the reason stated above, we are returning your petition for rule making.

Sincerely,

A handwritten signature in black ink, appearing to read "John A. Karousos".

John A. Karousos
Assistant Chief, Audio Division
Media Bureau

Enclosures


CERTIFICATE OF SERVICE

I, Katherine Pyeatt, hereby certify that on this 13th day of December, 2004, I caused copies of the foregoing "Counterproposal" to be placed in the U.S. Postal Service, first class postage prepaid, addressed to the following persons:

Rolanda F. Smith
Federal Communications Commission
Media Bureau-Audio Services Division
445 12th Street, S.W., Room 3-A224
Washington, D.C. 20554

Gene A. Bechtel, Esq.
1050 17th Street, N.W., Suite 600
Washington, D.C. 20036

Charles Crawford
4553 Bordeaux Ave.
Dallas, Texas 75205


Katherine Pyeatt
