



20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275 * Fax: 585-786-6280 * Email: wnyrbhn@r-ahec.org

** New information for the quarterly report appears in the purple, bold, italic font*

Project Leader(s) & Business Affiliations:

- Kenneth L. Oakley, PhD, FACHE – CEO & Project Coordinator
 - Email: wnyrbhn@r-ahec.org
- Kimberly R Cummins – Assistant Project Coordinator /Project Administrative Coordinator
 - Email: kcummins@r-ahec.org

Address:

Western New York Rural Area Health Education Center, Inc. (R-AHEC)
20 Duncan Street
PO BOX 152
Warsaw, NY 14569
Phone: 585-786-6275 Fax: 585-786-6280

Organization Legally & Financially Responsible:

Western New York Rural Area Health Education Center, Inc.

Brief Description how coordinated through state or region:

R-AHEC staff having been actively working to coordinate our Rural Pilot efforts with that of others in several different ways:

- 1) We have had three regional meetings of the Project Technical Working Group (TWG) comprising of CIO's and Network Directors of the partnering healthcare organizations.
- 2) We have had numerous meetings with the two Regional Health Information Organizations (RHIO) operating within our shared catchment area.
- 3) We have had two meetings with the Office of the Deputy Commissioner, NYS DOH Office of Information Technology Transformation, along with the two other RHCPP awardees in New York State. The focus is to ensure interoperability and interconnectivity between the three RHCPP projects in New York State.

July, 2009 ~ Quarterly Report

R-AHEC staff has been actively working to coordinate our Rural Pilot efforts with that of others in several different ways:

- 1) We have submitted the draft version of our proposed RFP for review by our coach.
- 2) We are in discussions with the two other RHCPP projects in NY State and with the NY State eHealth Collaborative about the sustainability plan for our project within the context of NY State's plans for a Broadband Health
- 3) We have conducted multiple information sessions with the carrier organizations in our region to provide them information about the FCC Rural Healthcare Broadband Project and to learn about their facilities, technologies and capabilities for offering rural broadband services care Network

October, 2009 ~ Quarterly Report

R-AHEC has been actively working to coordinate our Rural Pilot efforts with that of others in several different ways:

- 1) We are currently working with our coach for the finalization our proposed RFP and supporting documentation.
- 2) We have continued in discussions with the other two RHCPP projects in NY and with the NYState eHealth Collaborative. The Office of HIT at the NY State Department of Health is actively following the development of our RHCPP project.

R-AHEC has been actively working to coordinate our Rural Pilot efforts with that of others in several different ways:

- 1) Finalization our proposed RFP and supporting documentation, posted on USAC website 07/02/09.
- 2) Vendor responses were received on 08/17/09.
- 3) Bid Review committee was established for review of vendor responses and selection of vendor.
- 4) We have continued in discussions with the other two RHCPP projects in NY and with the NYState eHealth Collaborative. The Office of HIT at the NY State Department of Health is actively following the development of our RHCPP project.

January, 2010 ~ Quarterly Report

R-AHEC has been actively working to coordinate our Rural Pilot efforts with that of others in several different ways:

- 1) Finalized our proposed RFP and supporting documentation, posted on USAC website 07/02/09.
- 2) Vendor responses were received on 08/17/09.
- 3) Bid Review committee was established for review and selection of vendor responses and continues to move forward in this process.
- 4) We have continued in discussions with the other two RHCPP projects in NY and with the NYState eHealth Collaborative. The Office of HIT at the NY State Department of Health is actively following the development of our RHCPP project.

April, 2010 ~ Quarterly Report

R-AHEC has been actively working to coordinate our Rural Pilot efforts with that of others in several different ways:

- 1) Finalized our proposed RFP and supporting documentation, posted on USAC website 07/02/09.
- 2) Vendor responses were received on 08/17/09.
- 3) August, 2009 - February, 2010 A Bid Review committee reviewed all proposals received, held various meetings, and selected a vendor.
- 4) A letter of intent was delivered to the vendor and we are currently in contract negotiations

5) We have continued in discussions with the other two RHCPP projects in NY and with the NY State eHealth Collaborative. The Office of HIT at the NY State Department of Health is actively following the development of our RHCPP project.

July, 2010 ~ Quarterly Report

R-AHEC has been actively working to coordinate our Pilot efforts with that of others in several different ways:

- 1) Paperwork for FCL is being finalized.
- 2) Preparing for issuing RFP 02 & 03 in early August, 2010
- 3) Continued discussions with other RHCPP projects and the NY State eHealth Collaborative.

October, 2010 ~ Quarterly Report

R-AHEC has been actively working to coordinate our Pilot efforts with that of others in several different ways:

- 1) Funding Commitment Letter was issued in early September, 2010
- 2) Letter of Intent to commence work was sent within days of FCL issuance.
- 3) Prep work and document details for RFP 02 & 03 to be posted on USAC website for additional facilities.
- 4) Continued discussions with other RHCPP project, NY State eHealth Collaborative, and RHIOs.

January, 2011 ~ Quarterly Report

R-AHEC has been actively working to coordinate our Pilot efforts with that of others in several different ways:

- 1) Funding Commitment Letter – RFP 01 was issued in early September, 2010
- 2) Letter of Intent to commence work was sent within days of FCL issuance.
- 3) Several facilities were “live” in the January – April time frame.
- 4) RFP 02 was posted on the USAC website in mid December, 2010 for additional facilities, responses for RFP 02 were due on January 20, 2011 and were promptly reviewed by the Bid Review Committee.
- 5) A vendor has been selected and we are currently in the process of filing paperwork for an FCL issuance on RFP 02.
- 6) Continued discussions with other RHCPP project, NY State eHealth Collaborative, and RHIOs.

July, 2011 ~ Quarterly Report

R-AHEC has been actively working to coordinate our Pilot efforts with that of others in several different ways:

- 1) Funding Commitment Letter – RFP 01 was issued in early September, 2010
- 2) Letter of Intent to commence work was sent within days of FCL issuance.
- 3) Final Facility “Live” in May
- 4) RFP 02 was posted on the USAC website in mid December, 2010 for additional facilities, responses for RFP 02 were due on January 20, 2011 and were promptly reviewed by the Bid Review Committee.

- 5) A vendor has been selected and we are currently in the process of filing paperwork for an FCL issuance on RFP 02.
- 6) Continued discussions with other RHCPP project, NY State eHealth Collaborative, and RHIOs.

October, 2011 ~ Quarterly Report

R-AHEC has been actively working to coordinate our Pilot efforts with that of others in several different ways:

- 1) Funding Commitment Letter – RFP 01 was issued in early September, 2010
- 2) Letter of Intent to commence work was sent within days of FCL issuance.
- 3) Final Facility “Live” in May
- 4) RFP 02 was posted on the USAC website in mid December, 2010 for additional facilities, responses for RFP 02 were due on January 20, 2011 and were promptly reviewed by the Bid Review Committee.
- 5) A vendor was selected, paperwork processed for FCL issuance RFP 02.
- 6) Funding Commitment Letter 02 adding on an additional 10 facilities was issued in September, 2011. Facilities are expected to start going live by the end of November, 2011.
- 7) Funding Commitment Letter 03 adding on 1 additional connection was issued in mid October, 2011. This facility is expected to go live by the end of December, 2011.
- 8) R-AHEC hosted a conference called Exploring Creation of an Upstate NY Telehealth Network – Improving the Access to Care and Lowering Costs through Telehealth
- 9) Continued discussions with other RHCPP project, NYS Senators, Legislative Commission of Rural Resources, NY State eHealth Collaborative, and RHIOs.

January, 2012 ~ Quarterly Report

R-AHEC has been actively working to coordinate our Pilot efforts with that of others in several different ways:

- 1) Funding Commitment Letter – RFP 01 was issued in early September, 2010
- 2) Letter of Intent to commence work was sent within days of FCL issuance.
- 3) Final Facility “Live” in May
- 4) RFP 02 was posted on the USAC website in mid December, 2010 for additional facilities, responses for RFP 02 were due on January 20, 2011 and were promptly reviewed by the Bid Review Committee.
- 5) A vendor was selected, paperwork processed for FCL issuance RFP 02.
- 6) Funding Commitment Letter 02 adding on an additional 10 facilities was issued in September, 2011. Facilities are expected to start going live by the end of November, 2011.
- 7) Funding Commitment Letter 03 adding on 1 additional connection was issued in mid October, 2011. This facility is expected to go live by the end of December, 2011.
- 8) R-AHEC hosted a conference called Exploring Creation of an Upstate NY Telehealth Network – Improving the Access to Care and Lowering Costs through Telehealth

- 9) Continued discussions with other RHCPP project, NYS Senators, Legislative Commission of Rural Resources, NY State eHealth Collaborative, and RHIOs.
- 10) R-AHEC is currently doing a project reach out to collaborate with any additional facilities interested in participating in the WNY RBHN. We are hoping to post another RFP mid-late February 2012.

02. Facilities in Network

Facility Name	Address	City	State	Zip	County	Phone	Fax	Rural Urban Commuting Area (RUCA)	State Code	County Code	Census Tract	Not-for-Profit or For-Profit	Eligible	Why Eligible or Ineligible	NYS DOH Operating Certificate
Arnot Ogden Medical Center	600 Roe Ave	Elmira	New York	14905	Chemung	(607) 737-4100		1	36	015	0004.02	Not-For Profit	Yes	Non-Profit Health Care Entity	0701000H
Auburn Memorial Hospital	17 Lansing Street	Auburn	New York	13021	Cayuga	(315) 253-1760		4.2	36	011	0414.00	Not-For Profit	Yes	Non-Profit Health Care Entity	0501000H
Brooks Memorial Hospital	529 Central Ave	Dunkirk	New York	14048	Chautauqua	(716) 366-1111		4	36	013	0356.00	Not-For	Yes	Non-Profit Health Care Entity	0601000H
Catholic Health Systems	Seton Professional Building; 2121 Main Street; Suite 300	Buffalo	New York	14214	Erie	(716) 862-2400	(716) 862-2468	1	36	029	0052.01	Not-For Profit	Yes	Non-Profit Health Care Entity	multiple
Cattaraugus Indian Reservation Health Center	36 Thomas Indian School Drive	Irving	New York	14081	Chautauqua	(716) 532-5582	(716) 532-0110	4	36	013	9501.00	Not-For Profit	Yes	Community Health Center	-
Clifton Springs Hospital & Clinic	2 Coulter Road	Clifton Springs	New York	14432	Ontario	(315) 462-9561	(315) 462-3492	4.1	36	069	0503.01	Not-For Profit	Yes	Non-Profit Health Care Entity	3421000H
Erie County Medical Center (ECMC)	462 Grider Street	Buffalo	New York	14215	Erie	(716) 898-3000		1	36	029	0039.02	Not-For Profit	Yes	Non-Profit Health Care Entity	1401005H
Finger Lakes Migrant Health Care Project, Inc. (Bath)	117 East Steuben Street	Bath	New York	14810	Steuben	(607) 776-3063	(607) 776-1011	7.4	36	101	9612.00	Not-For Profit	Yes	FQHC	-
Finger Lakes Migrant Health Care Project, Inc. (Geneva)	601B Washington Street	Geneva	New York	14456	Ontario	(315) 781-8448	(315) 781-8444	4	36	069	0515.00	Not-For Profit	Yes	FQHC	-
Finger Lakes Migrant Health Care Project, Inc. (Newark)	513 W Union Street; Cannery Row Route 31	Newark	New York	14513	Wayne	(315) 331-4399	(315) 331-4398	4	36	117	0211.00	Not-For Profit	Yes	FQHC	-
Finger Lakes Migrant Health Care Project, Inc. (Seneca)	7160 Main Street	Ovid	New York	14521	Steuben	(607) 869-9766		3	36	099	9509.00	Not-For Profit	Yes	FQHC	-
Finger Lakes Migrant Health Care Project, Inc. (Penn Yan)	112 Kimball Ave	Penn Yan	New York	14527	Seneca	(315) 536-2752	(315) 536-4005	7	36	123	9905.00	Not-For Profit	Yes	FQHC	-
Finger Lakes Migrant Health Care Project, Inc. (Port Byron)	60 Main Street	Port Byron	New York	13160	Cayuga	(315) 776-9700	(315) 776-9701	5	36	011	0403.00	Not-For Profit	Yes	FQHC	-
Finger Lakes Migrant Health Care Project, Inc. (Sodus)	6692 Middle Road Suite 2100	Sodus	New York	14451	Wayne	(315) 483-1199	(315) 483-2451	1	36	117	0208.00	Not-For Profit	Yes	FQHC	-
Geneva General Hospital	196 North Street	Geneva	New York	14456	Ontario	(315) 787-4000		4	36	069	0517.00	Not-For Profit	Yes	Non-Profit Health Care Entity	3402000H
Ira Davenport Memorial Hospital, Inc.	7571 State Route 54	Bath	New York	14810	Steuben	(607) 776-8500		7.4	36	101	9614.00	Not-For Profit	Yes	Non-Profit Health Care Entity	5022000H
Jones Memorial Hospital	191 North Main Street; PO BOX 72	Wellsville	New York	14895	Allegany	(585) 596-4002		7	36	003	9507.00	Not-For Profit	Yes	Non-Profit Health Care Entity	0228000H
Kaleida Health	100 High Street	Buffalo	New York	14203	Erie	(716) 859-2732	(716) 859-3323	1	36	029	0031.00	Not-For Profit	Yes	Non-Profit Health Care Entity	multiple
Lakeshore Health Care Center	845 Routes 5 & 20	Irving	New York	14081	Chautauqua	(716) 951-7000	(716) 951-7046	7.1	36	013	0351.00	Not-For Profit	Yes	Rural Health Clinic	0427000H
Lakeside Health System	150 West Avenue	Brockport	New York	14420	Monroe	(585) 395-6095		1	36	055	0152.00	Not-For Profit	Yes	Non-Profit Health Care Entity	2728001H
Lionel R John Health Center	987 R.C. Hoag Drive	Salamanca	New York	14779	Cattaraugus	(716) 945-5894	(716) 945-0308	7.4	36	009	9621.00	Not-For Profit	Yes	Rural Health Clinic	-
Medina Memorial Health Care System	200 Ohio Street	Medina	New York	14103	Orleans	(585) 798-2000	(585) 798-8444	7	36	073	0404.00	Not-For Profit	Yes	Non-Profit Health Care Entity	3622000H
Mount St. Mary's Hospital and Health Center	5300 Military Road	Lewiston	New York	14092	Niagara	(716) 298-2173	(419) 844-6157	1	36	063	0244.04	Not-For Profit	Yes	Non-Profit Health Care Entity	3121001H
Niagara Falls Memorial Medical Center	621 Tenth Street	Niagara Falls	New York	14302	Niagara	(716) 278-4000		1	36	063	0212.00	Not-For Profit	Yes	Non-Profit Health Care Entity	3102000H
Nicholas H. Noyes Memorial Hospital	111 Clara Barton Street	Dansville	New York	14437	Livingston	(585) 335-6001		7.3	36	051	0314.00	Not-For Profit	Yes	Non-Profit Health Care Entity	2527000H
Noyes Memorial Hospital (Livingston Health Services)	50 South East Street	Geneseo	New York	14454	Livingston	(585) 243-9230	(585) 335-5881	7.3	36	051	0304.00	Not-For Profit	Yes	Non-Profit Health Care Entity	2527000H
Oak Orchard Community Health Center, Inc. (Albion Clinic)	245 South Main Street	Albion	New York	14411	Orleans	(585) 589-4519	(585) 637-4990	8.3	36	073	0407.00	Not-For Profit	Yes	FQHC	-
Oak Orchard Community Health Center, Inc. (Lyndonville Clinic)	77 South Main Street	Lyndonville	New York	14098	Orleans	(585) 637-3905	(585) 637-4990	3	36	073	4010.01	Not-For Profit	Yes	FQHC	-
Oak Orchard Community Health Center, Inc. (West Ave - Albion Clinic)	301 West Ave	Albion	New York	14411	Orleans	(585) 589-5613	(585) 589-0872	8.3	36	073	0407.00	Not-For Profit	Yes	FQHC	-
Oak Orchard Community Health Center, Inc. (West Ave - Brockport Clinic)	300 West Ave	Brockport	New York	14420	Monroe	(585) 637-3905	(585) 637-4990	3	36	055	0152.00	Not-For Profit	Yes	FQHC	-
Olean General Hospital	515 Main Street	Olean	New York	14760	Cattaraugus	(716) 373-2600	(716) 375-6394	4	36	009	9615.00	Not-For Profit	Yes	Non-Profit Health Care Entity	0401001H
Rochester General (Via Health)	333 Humboldt Street; PO BOX 10790	Rochester	New York	14610	Monroe	(585) 922-1651		1	36	055	0077.00	Not-For Profit	Yes	Non-Profit Health Care Entity	-
Schuyler Hospital	200 Steuben Street	Montour Falls	New York	14865	Schuyler	(607) 535-7121	(607) 535-9097	10.4	36	097	9504.00	Not-For Profit	Yes	Non-Profit Health Care Entity	4823700C
Soldiers & Sailors Memorial Hospital	418 North Main Street	Penn Yan	New York	14527	Seneca	(315) 787-4031		7.4	36	123	9902.00	Not-For Profit	Yes	Non-Profit Health Care	6120700C
St. James Mercy Health System	411 Canisteo Street	Hornell	New York	14843	Steuben	(607) 324-8113	(607) 324-8960	4	36	101	9608.00	Not-For Profit	Yes	Non-Profit Health Care Entity	5002001H
St. Joseph's Hospital	555 East Market Street	Elmira	New York	14901	Chemung	(607) 733-6541		1	36	015	0008.00	Not-For Profit	Yes	Non-Profit Health Care Entity	0701001H
The Resource Center	800 East Second Street	Jamestown	New York	14701	Chautauqua	(716) 483-2344		4	36	013	0301.00	Not-For Profit	Yes	Non-Profit Health Care Entity	060221R
Thompson Health	350 Parrish Street	Canandaigua	New York	14424	Ontario	(585) 396-6000	(585) 396-6477	4.1	36	069	0510.00	Not-For Profit	Yes	Non-Profit Health Care Entity	3429000H
TLC Health Network	845 Routes 5 & 20	Irving	New York	14081	Chautauqua	(716) 951-7000	(716) 951-7046	7.1	36	013	0351.00	Not-For Profit	Yes	Non-Profit Health Care Entity	0427000H
Tri-County Memorial Hospital	100 Memorial Drive	Gowanda	New York	14070	Cattaraugus	(716) 951-5034	(716) 532-8091	9.1	36	009	9604.00	Not-For Profit	Yes	Non-Profit Health Care Entity	0427000H
UB Family Medicine, Inc.	463 Grider Street	Buffalo	New York	14215	Erie	(716) 898-5212		1	36	029	0039.02	Not-For Profit	Yes	Teaching facility	-
UB Family Medicine of Amherst (UB Family Medicine, Inc.)	850 Hopkins Rd	Buffalo	New York	14221	Erie	716-898-4744	716-898-4750	1	36	029	0091.13	Not-For Profit	Yes	Teaching facility	-
UB Family Medicine, Inc. (Jefferson Family Medicine)	1315 Jefferson Ave	Buffalo	New York	14208	Erie	716-898-4744	716-898-4750	1	36	029	0033.02	Not-For Profit	Yes	Teaching facility	-
UB Family Medicine, Inc. (Sheridan)	2465 Sheridan Drive	Tonawanda	New York	14150	Erie	716-898-4744	716-898-4750	1	36	029	0080.01	Not-For Profit	Yes	Teaching facility	-
UB School of Medicine & Biomedical Sciences	155 Biomedical Education Building; 3435 Main Street	Buffalo	New York	14214	Erie	(716) 829-2975	(716) 829-2915	1	36	029	0046.02	Not-For Profit	Yes	Teaching facility	-
UB School of Medicine & Biomedical Sciences(350)	350 Main Street	Buffalo	New York	14202	Erie	(716) 829-2975	(716) 829-2915	1	36	029	0072.01	Not-For Profit	Yes	Teaching facility	-
United Memorial Medical Center	127 North Street	Batavia	New York	14020	Genesee	(585) 343-6030	(585) 344-7434	4.2	36	037	9508.00	Not-For Profit	Yes	Non-Profit Health Care Entity	1801000H
University @ Buffalo Neurosurgery	3 Gates Circle	Buffalo	New York	14209	Erie	(716) 887-5200		1	36	029	0063.02	Not-For Profit	Yes	Teaching facility	-
University @ Buffalo Neurosurgery (Sheridan/Dent)	3980 Sheridan Drive (dent tower)	Buffalo	New York	14226	Erie	716-887-5200		1	36	029	0092.00	Not-For Profit	Yes	Teaching facility	-
University of Rochester Medical Center (URMC)	400 Elmwood Ave	Rochester	New York	14627	Monroe	585-275-7685		1	36	055	0038.01	Not-For Profit	Yes	Non-Profit Health Care	2701005H
University Orthopaedic Services, Inc	3435 Main Street	Buffalo	New York	14214	Erie	(716) 829-3670	(716) 829-3514	1	36	029	0046.02	Not-For Profit	Yes	Teaching facility	-
University Orthopaedic Services, Inc (Harlem Road)	4949 Harlem Road	Buffalo	New York	14226	Erie	716-829-3670	716-829-3514	1	36	029	0094.02	Not-For Profit	Yes	Teaching facility	-
WCA Hospital	207 Foote Avenue; PO BOX 840	Jamestown	New York	14702	Chautauqua	(716) 487-0141	(716) 664-8336	4	36	013	0306.00	Not-For Profit	Yes	Non-Profit Health Care	0602001H
Western New York Rural Area Health Education Center	20 Duncan Street, PO BOX 152	Warsaw	New York	14569	Wyoming	(585) 786-6275	(585) 786-6280	7.3	36	121	9905.00	Not-For Profit	No	Ineligible	-
Westfield Memorial Hospital	189 East Main Street	Westfield	New York	16544	Chautauqua	(716) 326-4921		7.4	36	013	0365.00	Not-For Profit	Yes	Non-Profit Health Care Entity	0632000H
Wyoming County Community Health System	400 North Main Street	Warsaw	New York	14569	Wyoming	(585) 786-8940	(585) 786-1222	7	36	121	9905.00	Not-For Profit	Yes	Non-Profit Health Care Entity	6027000H

**Indicates facility temporarily on hold*

** Updated/New information for the quarterly report appears in the purple, bold, italic font*



20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275

*

Fax: 585-786-6280

*

Email: wnyrbhn@r-ahec.org

NETWORK NARRATIVE

** New information for the quarterly report appears in the purple, bold, italic font*

A) Brief Description of backbone network of dedicated health care network (e.g. MPLS Network, carrier-provided VPN, a SONET ring)

The Western New York Rural Healthcare Broadband Network (WNY RHBN) is a dedicated Internet Protocol (IP)-based broadband healthcare network that will provide each partner facility a minimum of 10 Megabits per second (Mbps) minimum scalable upwards bandwidth, based upon facility, connecting them over a secure enterprise wide-area-network, with Quality of Service (QoS) features and the option of connecting to the commercial Internet & to Internet 2. When fully implemented, the WNY RBHN will bring services to rural communities through innovative health information technology applications, including telemedicine, imaging, and electronic medical records.

B) Explanation of how health care provider sites will connect to (or access) the network, including access technologies/services and transmission speeds

Each partner facility has a minimum of 10 Megabits per second (Mbps) minimum scalable upwards bandwidth, based upon facility, connecting them over a secure enterprise wide-area-network, with Quality of Service (QoS) features blending MPLS and Internet via Domain Name System (DNS) hosting. The network also features Virtual Local Area Network (VLAN) meaning each of the facilities on the network can access each other privately via the privately advertised VLAN IP address.

C) Explanation of how and where network will connect to a national backbone such as NLR or Internet2

It is proposed that the Western New York Rural Healthcare Broadband Network (WNY RHBN) - a dedicated Internet Protocol (IP)-based broadband healthcare network - has the ability to connect to Internet2 through the nearest NYSERNET point of presence (POP) - NYSERNET is the agency that is responsible for Internet2 connectivity in New York State. At this time as facilities continue to go "live" on the MPLS Network we have elected not to connect to Internet2 however, should a facility desire to utilize Internet2 we will work with all appropriate parties to ensure that ability.

D) Number of miles of fiber construction, and whether the fiber is buried or aerial

Between all of the facilities there is a combined total of over 4,000 total fiber miles. Within this 4,000 miles there is a combination of aerial, buried, and conduit style fiber transport.



20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275

*

Fax: 585-786-6280

*


Email: wnyrbhn@r-ahec.org

E) Special systems or services for network management or maintenance (if applicable) and where such systems reside or are based.

Each of the facilities on this network are connected with a pro-active management of the network with the Advanced Managed Router. This Advanced Managed Router includes monitored services with auto-notification “PING” monitoring, electronic notifications (including e-mail and pager messaging), trouble resolution, device default, and configuration management.

Facility Name	Address	City	State	How is facility connection provided?	Service and/or Speed	Gateway to NLR, Internet 2, or Public Internet	Site Equipment	Site Equipment Manufacturer	Site Equipment Model	Circuit ID
Brooks Memorial Hospital	529 Central Ave	Dunkirk	New York	Carrier-Provided Services	20 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413684/100/PU A /FED
Clifton Springs Hospital & Clinic	2 Coulter Road	Clifton Springs	New York	Carrier-Provided Services	30 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413685/100/PU A /FED
Finger Lakes Migrant Health Care Project, Inc. (Geneva)	601B Washington Street	Geneva	New York	Carrier-Provided Services	20 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413687/100/PU A /FED
Finger Lakes Migrant Health Care Project, Inc. (Port Byron)	60 Main Street	Port Byron	New York	Carrier-Provided Services	20 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413688/100/PU A /FED
Finger Lakes Migrant Health Care Project, Inc. (Sodus)	6692 Middle Road Suite 2100	Sodus	New York	Carrier-Provided Services	20 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413699/100/PU A /FED
Ira Davenport Memorial Hospital, Inc.	7571 State Route 54	Bath	New York	Carrier-Provided Services	45 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413686/100/PU A /FED
Jones Memorial Hospital	191 North Main Street; PO BOX 72	Wellsville	New York	Carrier-Provided Services	20 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413690/100/PU A /FED
Lakeshore Health Care Center	845 Routes 5 & 20	Irving	New York	Carrier-Provided Services	20 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413698/100/PU A /FED
Lakeside Health System	150 West Avenue	Brockport	New York	Carrier-Provided Services	20 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413691/100/PU A /FED
Medina Memorial Health Care System	200 Ohio Street	Medina	New York	Carrier-Provided Services	20 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413692/100/PU A /FED
Mount St. Mary's Hospital and Health Center	5300 Military Road	Lewiston	New York	Carrier-Provided Services	10 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413693/100/PU A /FED

Facility Name	Address	City	State	How is facility connection provided?	Service and/or Speed	Gateway to NLR, Internet 2, or Public Internet	Site Equipment	Site Equipment Manufacturer	Site Equipment Model	Circuit ID
Nicholas H. Noyes Memorial Hospital	111 Clara Barton Street	Dansville	New York	Carrier-Provided Services	20 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413694/100/PUA /FED
Oak Orchard Community Health Center, Inc. (Albion Clinic)	245 South Main Street	Albion	New York	Carrier-Provided Services	20 Mbps	Public Internet	Router	Adtran	4430	74/FEDO/413703/100/PUA /FED
Oak Orchard Community Health Center, Inc. (Lyndonville Clinic)	77 South Main Street	Lyndonville	New York	Carrier-Provided Services	10 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413700/100/PUA /FED
Oak Orchard Community Health Center, Inc. (West Ave - Brockport Clinic)	300 West Ave	Brockport	New York	Carrier-Provided Services	25 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413695/100/PUA /FED
Olean General Hospital	515 Main Street	Olean	New York	Carrier-Provided Services	10 Mbps	Public Internet	Router	Adtran	4430	74/FEDO/413704/100/PUA /FED
The Resource Center	800 East Second Street	Jamestown	New York	Carrier-Provided Services	10 Mbps	Public Internet	Router	Adtran	4430	74/FEDO/413707/100/PUA /FED
Schuyler Hospital	200 Steuben Street	Montour Falls	New York	Carrier-Provided Services	20 Mbps	Public Internet	Router	Adtran	4430	74/FEDO/413707/100/PUA /FED
St. James Mercy Health System	411 Canisteo Street	Hornell	New York	Carrier-Provided Services	45 Mbps	Public Internet	Router	Adtran	4430	74/FEDO/413706/100/PUA /FED
Thompson Health	350 Parrish Street	Canandaigua	New York	Carrier-Provided Services	20 Mbps	Public Internet	Router	Adtran	4430	74/FEDO/413708/100/PUA /FED
United Memorial Medical Center	127 North Street	Batavia	New York	Carrier-Provided Services	20 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413696/100/PUA /FED
WCA Hospital	207 Foote Avenue; PO BOX 840	Jamestown	New York	Carrier-Provided Services	45 Mbps	Public Internet	Router	Adtran	4430	40/FEDO/413697/100/PUA /FED
Wyoming County Community Health System	400 North Main Street	Warsaw	New York	Carrier-Provided Services	20 Mbps	Public Internet	Router	Adtran	4430	74/FEDO/413702/100/PUA /FED

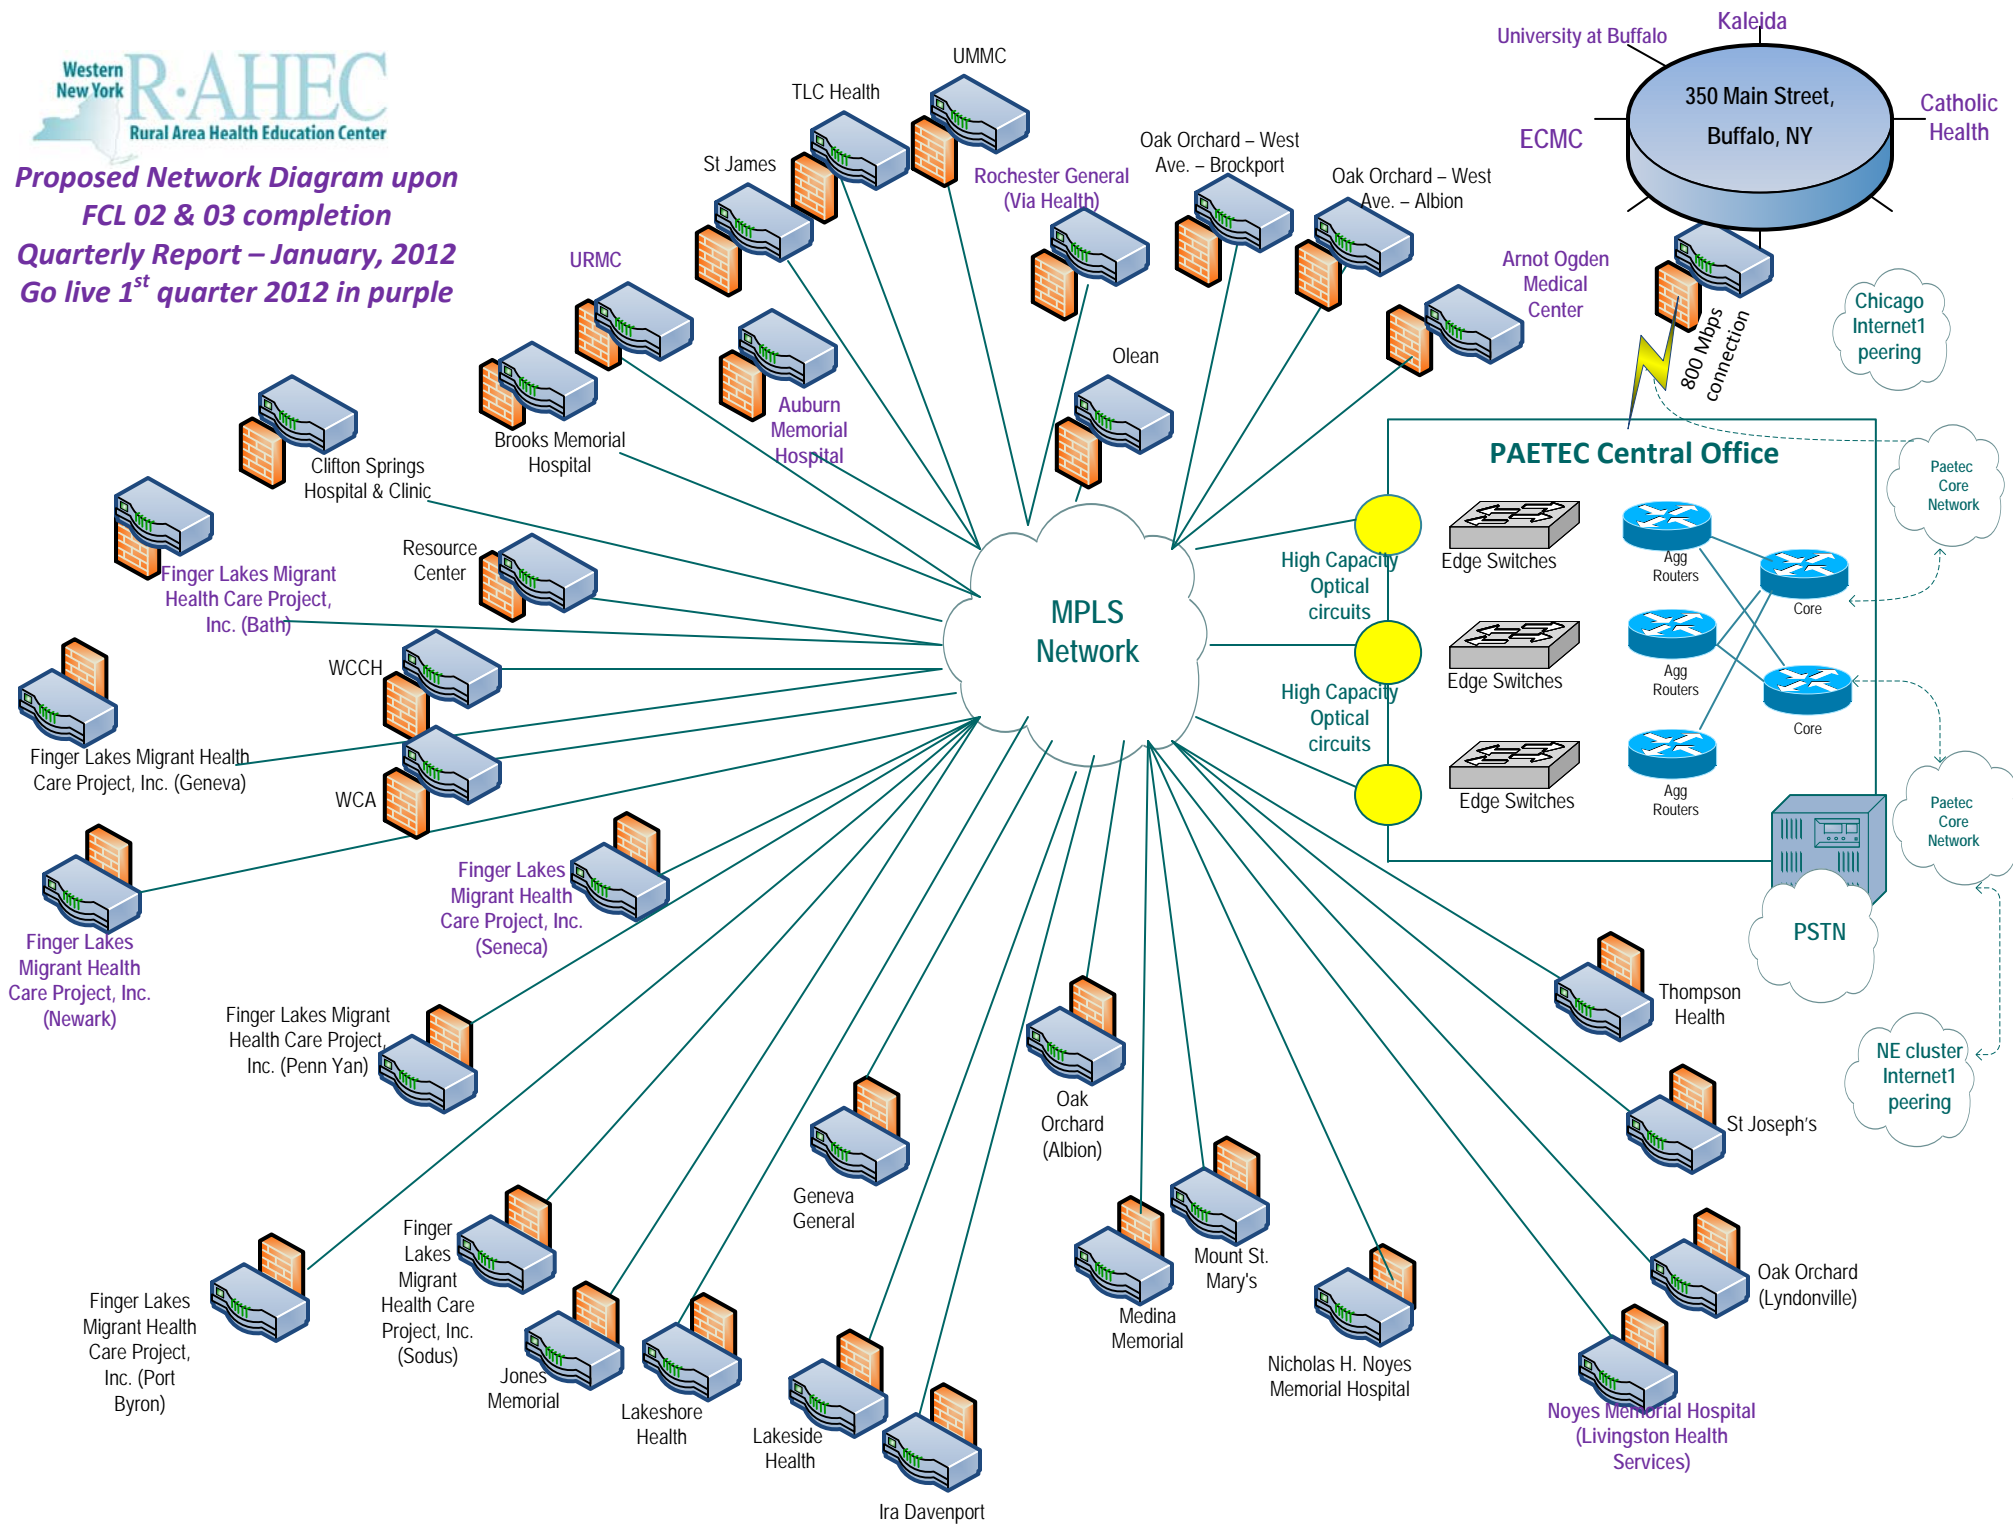

06. Recurring & Non Costs

<u>Expense Incurred by:</u>	<u>Type Of Cost</u>	<u>Allocation of Cost</u>	<u>Recurring or Non-Recurring?</u>	<u>Eligible/Ineligible ?</u>	<u>Contributions from Other Sources ?</u>	<u>Source of Contribution</u>	<u>Source Name:</u>	<u>Amount:</u>
Western New York Rural AHEC (January 01, 2008 - June 30, 2008)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 18,568.52
Western New York Rural AHEC (January 01, 2008 - June 30, 2008)	RFP Development	Subcontracted Services - RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 26,207.59
Western New York Rural AHEC (July 01, 2008 - September 30, 2008)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 8,955.51
Western New York Rural AHEC (July 01, 2008 - September 30, 2008)	RFP Development	Subcontracted Services - RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 6,972.09
Western New York Rural AHEC (October 01, 2008 - December 31, 2008)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 6,408.12
Western New York Rural AHEC (October 01, 2008 - December 31, 2008)	RFP Development	Subcontracted Services - RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 24,629.65
Western New York Rural AHEC (January 01, 2009 - February 28, 2009)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 7,035.18
Western New York Rural AHEC (January 01, 2009 - February 28, 2009)	RFP Development	Subcontracted Services - RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 7,801.00
Western New York Rural AHEC (March 01, 2009 - May 31, 2009)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 14,996.73
Western New York Rural AHEC (March 01, 2009 - May 31, 2009)	RFP Development	Subcontracted Services - RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 7,082.70
Western New York Rural AHEC (June 01, 2009 - September 30, 2009)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 14,402.77
Western New York Rural AHEC (June 01, 2009 - September 30, 2009)	RFP Development	Subcontracted Services - RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 16,773.36
Western New York Rural AHEC (October 01, 2009 - November 30, 2009)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 10,328.09
Western New York Rural AHEC (October 01, 2009 - November 30, 2009)	RFP Development	Subcontracted Services - RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 5,540.00
Western New York Rural AHEC (December 2009)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 14,714.79
Western New York Rural AHEC (December 2009)	RFP Development	Subcontracted Services - RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 10,717.84
Western New York Rural AHEC (January 01, 2010 - March 31, 2010)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 27,856.15
Western New York Rural AHEC (April, 2010)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 18,981.02
Western New York Rural AHEC (May, 2010)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 11,426.97
Western New York Rural AHEC (June, 2010)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 20,346.08
Western New York Rural AHEC (July, 2010)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 5,463.24
Western New York Rural AHEC (August, 2010)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 4,756.17

06. Recurring & Non Costs

<u>Expense Incurred by:</u>	<u>Type Of Cost</u>	<u>Allocation of Cost</u>	<u>Recurring or Non-Recurring?</u>	<u>Eligible/Ineligible ?</u>	<u>Contributions from Other Sources ?</u>	<u>Source of Contribution</u>	<u>Source Name:</u>	<u>Amount:</u>
Western New York Rural AHEC (September, 2010)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 5,618.67
Western New York Rural AHEC (October, 2010)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 10,951.30
Western New York Rural AHEC (November, 2010) *revised	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 11,167.39
Western New York Rural AHEC (December, 2010) *revised	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 15,435.68
Western New York Rural AHEC (January, 2011)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 5,782.70
Western New York Rural AHEC (February, 2011)	RFP Development	RFP Design	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 5,285.35
Western New York Rural AHEC (March, 2011)	Other Recurring Costs	Administrative	Recurring	To Be Determined	Yes	Local	Western New York Rural AHEC	\$ 5,411.72
Western New York Rural AHEC (April, 2011)	Other Recurring Costs	Administrative	Recurring	To Be Determined	Yes	Local	Western New York Rural AHEC	\$ 10,536.44
Western New York Rural AHEC (May, 2011)	Other Recurring Costs	Administrative	Recurring	To Be Determined	Yes	Local	Western New York Rural AHEC	\$ 7,210.01
Western New York Rural AHEC (Invoice 01)	Construction	Ethernet Buildout - synchronous up to 100 Mbps	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 13,750.00
Western New York Rural AHEC (Invoice 01)	Other - Equipment	Equipment - Routers	Non-Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 12,852.00
Western New York Rural AHEC (Invoice 01)	Monthly Recurring - Ethernet		Recurring	Eligible	Yes	Local	Western New York Rural AHEC	\$ 104,900.50
Western New York Rural AHEC (June, 2011)	Other Recurring Costs	Administrative	Recurring	To Be Determined	Yes	Local	Western New York Rural AHEC	\$ 12,098.04
Western New York Rural AHEC (July, 2011)	Other Recurring Costs	Administrative	Recurring	To Be Determined	Yes	Local	Western New York Rural AHEC	\$ 2,244.91
Western New York Rural AHEC (August, 2011)	Other Recurring Costs	Administrative	Recurring	To Be Determined	Yes	Local	Western New York Rural AHEC	\$ 13,191.94
Western New York Rural AHEC (September, 2011)	Other Recurring Costs	Administrative	Recurring	To Be Determined	Yes	Local	Western New York Rural AHEC	\$ 9,137.53
<i>Western New York Rural AHEC (October, 2011)</i>	<i>Other Recurring Costs</i>	<i>Administrative</i>	<i>Recurring</i>	<i>To Be Determined</i>	<i>Yes</i>	<i>Local</i>	<i>Western New York Rural AHEC</i>	<i>\$ 7,244.37</i>
<i>Western New York Rural AHEC (November, 2011)</i>	<i>Other Recurring Costs</i>	<i>Administrative</i>	<i>Recurring</i>	<i>To Be Determined</i>	<i>Yes</i>	<i>Local</i>	<i>Western New York Rural AHEC</i>	<i>\$ 14,105.50</i>

Total: *\$ 538,319.10*

** New information for the quarterly report appears in the purple, bold, italic font*



20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275

*

Fax: 585-786-6280

*

Email: wnyrbhn@r-ahec.org

** New information for the quarterly report appears in the purple, bold, italic font*

Explanation of Costs:

A) Explanation of Costs identified, allocated, and apportioned to both eligible and ineligible network participants.

The costs that we are identifying are eligible expenses that were incurred in the RFP Design and Development phase of the project. Within this category the key areas of focus have been developing the engineering and design criteria for the RFP and coordinating carrier information sessions with carrier organizations in our region to learn about their technologies, facilities and capabilities to design and implement rural broadband networks.

Construction Costs: Ethernet Build out - synchronous up to 800 Mbps

Other – Equipment: Equipment – Routers for the MPLS Connection. The equipment in this instance was ADTRAN 4430 routers for the actual connection of the network via the routers.

Monthly Recurring – Ethernet: Monthly recurring charge for connection. Speeds for the facilities vary based upon facility need.

B) Describe source of funds from:

i) Eligible Pilot Program Network Participants.

In order to address the subsidy, R-AHEC will be utilizing the FCC funding by providing varying subsidy for the facilities with a maximum subsidy being 80% FCC / 20% Facility. As the facility bandwidth increases to 100 Mbps and upwards the facilities will be paying a maximum subsidy of 75% FCC/ 25% Facility.

ii) Ineligible Pilot Program network participants.

R-AHEC does not own the network. Appropriate, yet ineligible entities, which wish to join the WNY RBHN, will pay for their own Installation, Equipment, Monthly Recurring and service charges for broadband directly to our chosen vender. R-AHEC and the WNY RBHN will not pay for any services to any ineligible facilities. To date there are no ineligible facilities on the network.

C) Show contributions from all other sources (e.g. local, state, and federal sources, and other grants)

i) Identify sources of financial support and anticipated revenues that is paying for costs not covered by the fund and by Pilot Program

R-AHEC is pursuing other Federal and NY State grant funding opportunities to procure equipment and services ineligible to the FCC Pilot Program funding. In addition each of the partners of the WNY RBHN agreed to contribute via sliding scale fee to defray some of the administration of the program (\$5,000 rural, \$10,000 urban, \$25,000 academic). In addition to the initial administrative funds from the partners of the program R-AHEC just decided on a sliding scale fee for future work with the facilities some of this work includes but is not limited to: applications work, recurring invoicing, and continual sustainability plans and work for the



R·AHEC

Rural Area Health Education Center

20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275

*

Fax: 585-786-6280

*

Email: wnyrbhn@r-ahec.org

** New information for the quarterly report appears in the purple, bold, italic font*

future. This sliding scale fee is based upon the bandwidth the facility has. Sliding scale fee is currently:

<u>RATE CHART</u>	
<u>FCC Facility Bandwidth</u>	<u>Annual Fee</u>
10 – 19	\$1,750.00
20 – 29	\$2,250.00
30 – 39	\$2,750.00
40 – 49	\$3,250.00
50 – 59	\$3,750.00
60 – 69	\$4,250.00
70 – 79	\$4,750.00
80 – 89	\$5,250.00
90 – 99	\$5,750.00
100+	<i>negotiated</i>

ii) Identify the respective amounts and remaining time for such assistance.

At this time we are still in the process of identifying where any additional respective amounts and time frames for the assistance will be coming from as we are still in the process of adding on additional facilities and starting the applications/usages (Please see Section C, subsection i)

D) Explain how selected participants 15%-(for all purposes of our project the facilities are paying a minimum of 20% varying based on bandwidth need) contribution is helping to achieve both the selected participant's identified goals and objectives and the overarching goals of the Pilot Program.

We are currently continuing to connect facilities now and are expecting to start billing within the next few weeks. However, all Pilot Program Participants are in agreement that they will contribute a minimum of twenty percent towards the bandwidth and broadband services provisioned for their respective facilities. We feel that having the facilities pay a larger percentage shows their commitment to not only the creation of the WNY RBHN but also the commitment that they have in the Pilot Program as well.



20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275

*

Fax: 585-786-6280

*

Email: wnyrbhn@r-ahec.org

** New information for the quarterly report appears in the purple, bold, italic font*

Ineligible Entity Requirements

A) Identify any technical or non-technical requirements or procedures necessary for ineligible entities to connect to the participant's network.

- 1) Confirm the ineligibility of the entity with FCC/USAC
- 2) Convey the ineligibility to the entity
- 3) Identify the entity's requirement for the broadband services over the WNY RBHN and ensure that the requirements are for acceptable healthcare applications
- 4) Identify and convey the costs of broadband access to the entity
- 5) Sign the Memorandum of Understanding with the entity
- 6) Proceed with broadband service provisioning



20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275 * Fax: 585-786-6280 * Email: wnyrbhn@r-ahec.org

** New information for the quarterly report appears in the purple, bold, italic font*

MANAGEMENT PLAN & SCHEDULE

Management Team:

Kenneth Oakley (Project Coordinator): Phone: 585-344-1022 Email: koakley@r-ahec.org

Kimberly Cummins (APC/Program Coordinator): Phone: 585-519-2511

Email: kcummins@r-ahec.org

First Quarterly Report ~ July 30, 2008

Projected Schedule*:

Mid to Late October 2008 - Complete Draft RFP and submit for review

Mid November 2008 - Submission of 465 & RFP

January 2009 thru February 2009 - Competitive Bidding Process

March 2009 - Review and selection of vendor(s) for project.

March-April 2009 - Submission of 466-A & Supporting information, Certification by vendor(s)

May 2009 - Funding Commitment Letters

June 2009 - Submission of 467 & Supporting information

July 2009 - Begin project build out.

Second Quarterly Report ~ October 30, 2008

Projected Schedule*:

Late October 2008 thru Early November 2008 - Complete Draft RFP and submit for review

Late November 2008 thru mid December 2008 - Submission of 465 & RFP

Late December 2008 thru late January 2009 - Competitive Bidding Process

February 2009 thru mid March 2009- Review and selection of vendor(s) for project.

Late March thru mid April 2009 - Submission of 466-A & Supporting information, Certification by vendor(s)

Late April 2009 thru early May 2009 - Funding Commitment Letters issued

Late May 2009 thru early June 2009 - Submission of 467 & Supporting information

Mid June 2009- Begin project build out.

Third Quarterly Report ~ January 30, 2009

Projected Schedule*:

End of December 2008 thru early January 2009 - Complete Draft RFP and submit for review (submitted for review)

Mid January 2009- Submission of 465 & 465 attachment (Completed)

Late January 2009 thru Early February 2008 - RFP posted on web & competitive bidding process

Late February 2009 thru Mid March 2009- Review and selection of vendor(s) for project.

Late March 2009 - Submission of 466-A & Supporting information, Certification by vendor(s)

Early April 2009 thru Mid April 2009 - Funding Commitment Letters issued

Late April 2009 thru early May 2009 - Submission of 467 & Supporting information

Mid May 2009- Begin project build out.



20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275

*

Fax: 585-786-6280

*

Email: wnyrbhn@r-ahec.org

** New information for the quarterly report appears in the purple, bold, italic font*

Fourth Quarterly Report ~ March 30, 2009

Late April 2009 thru Early May 2009 - Final approval on RFP submission & supporting docs

Late May 2009 thru Early June 2009 - 45 day waiting period

Mid June 2009 - Selection of a vendor(s) for the project

Mid June 2009 - Submission of 466-A & Supporting information, Certification by vendor(s)

Late June 2009 - Funding Commitment Letters issued

Late June 2009 thru Early July 2009 - Submission of 467 & Supporting Information

Mid July - Begin project build out.

Fifth Quarterly Report ~ July 30, 2009

Early July, 2009 - final approval of RFP and supporting documentation, submission & posting

Mid July, 2009 thru Mid August, 2009 - 45 day waiting period. Vendor Questions

Mid August, 2009 thru Early September, 2009- review documents & selection of vendor(s)

Early September, 2009 thru Mid September, 2009 - Submission of 466-A & Supporting Info, Certification of Vendor(s)

Late September, 2009 - Funding Commitment Letter issued

Late September, 2009 thru Early October, 2009 - Submission of 467 & Supporting documentation in addition to the starting of project build out.

Sixth Quarterly Report ~ October 30, 2009

Early July, 2009 - final approval of RFP and supporting documentation, submission & posting

Mid July, 2009 thru Mid August, 2009 - 45 day waiting period. Vendor Questions

Mid August, 2009 thru End October, 2009- review documents & selection of vendor(s)

Early November, 2009 thru Mid November, 2009 - Submission of 466-A & Supporting Info, Certification of Vendor(s)

Late November, 2009 - Funding Commitment Letter issued

Late November, 2009 thru Early December, 2009 - Submission of 467 & Supporting documentation in addition to the starting of project build out.

Seventh Quarterly Report ~ January 29, 2010

Early July, 2009 - final approval of RFP and supporting documentation, submission & posting

Mid July, 2009 thru Mid August, 2009 - 45 day waiting period. Vendor Questions

Mid August, 2009 thru End January, 2010 - review of submitted documents & vendor selection

Early to Mid February, 2009 thru Mid November, 2009 - Submission of 466-A & Supporting Info, Certification of Vendor(s)

Late February 2010 thru Early March 2010- Funding Commitment Letter issued

March 2010- Submission of 467 & Supporting documentation in addition to the starting of project builds out.



20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275

*

Fax: 585-786-6280

*

Email: wnyrbhn@r-ahec.org

** New information for the quarterly report appears in the purple, bold, italic font*

Eighth Quarterly Report ~ April 29, 2010

Early July, 2009 - final approval of RFP and supporting documentation, submission & posting

Mid July, 2009 thru Mid August, 2009 - 45 day waiting period. Vendor Questions

Mid August, 2009 thru End January, 2010 - review of submitted documents & vendor selection

Early to Mid February, 2010 - final selection of a vendor

March, 2010 - April, 2010 - contract negotiations

Early May 2010 - Submission of 466-A, contract & Supporting Info, Certification of Vendor

Mid to Late May 2010 - Funding Commitment Letter issued

June 2010 - Submission of 467 & Supporting documentation in addition to project build out.

August/September 2010 - Build out

Ninth Quarterly Report ~ July, 2010

Early July, 2009 - final approval of RFP and supporting documentation, submission & posting

Mid July, 2009 thru Mid August, 2009 - 45 day waiting period. Answered vendor questions

Mid August, 2009 thru End January, 2010 - review of submitted documents & vendor selection

Early to Mid February, 2010 - final selection of a vendor

March, 2010 - April, 2010 - contract negotiations

Early May 2010 through early August 2010 - Submission of 466-A, contract & Supporting Info, Certification of Vendor

Early August - FCL issued; as well as RFP #02 & #03 posted on USAC website

Mid August - Submission of 467 & Supporting documentation in addition to the starting of project build out.

Late August/September 2010 - Build out

Tenth Quarterly Report – October, 2010

Early July, 2009 - final approval of RFP and supporting documentation, submission & posting

Mid July, 2009 thru Mid August, 2009 - 45 day waiting period. Answered questions from vendors

Mid August, 2009 thru End January, 2010 - review of submitted documents & selection of vendor(s)

Early to Mid February, 2010 - final selection of a vendor

March, 2010 - April, 2010 - contract negotiations

Early May 2010 through early August 2010 - Submission of 466-A, contract, Certification of Vendor

Early September, 2010 - Funding Commitment Letter issued

Mid September – PAETEC commences work on facility build outs

Late October, 2010 – first facilities begin to roll out live.

November, 2010 – Facilities continue to become live. RFP #02 & #03 posted on USAC website

December, 2010 through January 2010 – applications commence



20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275

*

Fax: 585-786-6280

*

Email: wnyrbhn@r-ahec.org

** New information for the quarterly report appears in the purple, bold, italic font*

11th Quarterly Report – January, 2011

Early July, 2009 - final approval of RFP and supporting documentation, submission & posting
Mid July, 2009 thru Mid August, 2009 - 45 day waiting period. Answered questions from vendors
Mid August, 2009 thru End January, 2010 - review of submitted documents & selection of vendor(s)
Early to Mid February, 2010 - final selection of a vendor
March, 2010 - April, 2010 - contract negotiations
Early May 2010 through early August 2010- Submission of 466-A, contract, Certification of Vendor
Early September, 2010- Funding Commitment Letter issued
Mid September, 2010 through mid February, 2011 – PAETEC commences facility build outs
Late November, 2010 – first facilities begin to roll out live.
December, 2010 – Facilities continue to become live. RFP #02 posted on USAC website
December, 2010 through January 2011 – F.A.Q on RFP 02, build out of facilities, invoicing
Late January 2011 – end February, 2011 – Selection of vendor for RFP 02
Mid March, 2011 – RFP 03 for additional facilities if monies allow

12th Quarterly Report – April, 2011

Early July, 2009 - final approval of RFP and supporting documentation, submission & posting
Mid July, 2009 thru Mid August, 2009 - 45 day waiting period. Answered questions from vendors
Mid August, 2009 thru End January, 2010 - review of submitted documents & selection of vendor(s)
Early to Mid February, 2010 - final selection of a vendor
March, 2010 - April, 2010 - contract negotiations
Early May 2010 through early August 2010- Submission of 466-A, contract, Certification of Vendor
Early September, 2010- Funding Commitment Letter issued
Mid September, 2010 through mid February, 2011 – PAETEC begins work on facility build outs
Late November, 2010 – first facilities begin to roll out live.
December, 2010 – Facilities continue to become live. RFP #02 posted on USAC website
December, 2010 through January 2011 – F.A.Q on RFP 02, continue building out of facilities
Late January 2011 – end February, 2011 – Selection of vendor for RFP 02
March, 2011 – July, 2011 – finalizing invoicing with vendor. Submission of 1st invoice.



20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275

*

Fax: 585-786-6280

*

Email: wnyrbhn@r-ahec.org

** New information for the quarterly report appears in the purple, bold, italic font*

13th Quarterly Report – July, 2011

Early July, 2009 - final approval of RFP and supporting documentation, submission & posting

Mid July, 2009 thru Mid August, 2009 - 45 day waiting period. Answered questions from vendors

Mid August, 2009 thru End January, 2010 - review of submitted documents & selection of vendor(s)

Early to Mid February, 2010 - final selection of a vendor

March, 2010 - April, 2010 - contract negotiations

Early May 2010 through early August 2010- Submission of 466-A, contract, Vendor Certification.

Early September, 2010- Funding Commitment Letter issued

Mid September, 2010 through mid February, 2011 – PAETEC begins work on facility build outs

Late November, 2010 – first facilities begin to roll out live.

December, 2010 – Facilities continue to go live. As well as RFP #02 posted on USAC website

December, 2010 through January 2011 – F.A.Q on RFP 02, continue building out of facilities

Late January 2011 – end February, 2011 – Selection of vendor for RFP 02

March, 2011 – July, 2011 – finalizing invoicing with vendor. Submission of 1st invoice.

September, 2011 – additional RFP 03 and FCL's of additional facilities

Late October, 2011 – November – review of vendor submissions

November – December – Bid Review Committee selection of vendor

December – January – documentation completed for issuance of FCL

14th Quarterly Report – October, 2011 ** Timeline provided is best case scenario*

Early July, 2009 - final approval of RFP and supporting documentation, submission & posting

Mid July, 2009 thru Mid August, 2009 - 45 day waiting period. Answered questions from vendors

Mid August, 2009 thru End January, 2010 - review of submitted documents & selection of vendor(s)

Early to Mid February, 2010 - final selection of a vendor

March, 2010 - April, 2010 - contract negotiations

Early May 2010 through early August 2010- Submission of 466-A, contract, Vendor Certification.

Early September, 2010- Funding Commitment Letter issued

Mid September, 2010 through mid February, 2011 – PAETEC begins work on facility build outs

Late November, 2010 – first facilities begin to roll out live.

December, 2010 – Facilities continue to go live. As well as RFP #02 posted on USAC website

December, 2010 through January 2011 – F.A.Q on RFP 02, continue building out of facilities

Late January 2011 – end February, 2011 – Selection of vendor for RFP 02

March, 2011 – July, 2011 – finalizing invoicing with vendor. Submission of 1st invoice.

Late May, 2011 – FCL 01 facilities all live

September – Early October, 2011 – FCL's of additional facilities

November, 2011 – outreach for additional partners

Late November - December – RFP 03 posted on USAC website; as well as Funding Commitment Letter 02 facilities and Funding Commitment Letter 03 facilities live on WNY RBHN.

January, 2012 – Bid Review Committee selection of vendor

Late February – Mid March, 2012 – documentation completed for issuance of FCL

Early – Late March, 2012 – review regular program to see facilities that qualify and start processes to add them on to WNY RBHN.



20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275

*

Fax: 585-786-6280

*

Email: wnyrbhn@r-ahec.org

** New information for the quarterly report appears in the purple, bold, italic font*

15th Quarterly Report – January, 2012* Timeline provided is best case scenario

Early July, 2009 - final approval of RFP and supporting documentation, submission & posting

Mid July, 2009 thru Mid August, 2009 - 45 day waiting period. Answered questions from vendors

Mid August, 2009 thru End January, 2010 - review of submitted documents & selection of vendor(s)

Early to Mid February, 2010 - final selection of a vendor

March, 2010 - April, 2010 - contract negotiations

Early May 2010 through early August 2010- Submission of 466-A, contract, Vendor Certification.

Early September, 2010- Funding Commitment Letter issued

Mid September, 2010 through mid February, 2011 – PAETEC begins work on facility build outs

Late November, 2010 – first facilities begin to roll out live.

December, 2010 – Facilities continue to go live. As well as RFP #02 posted on USAC website

December, 2010 through January 2011 – F.A.Q on RFP 02, continue building out of facilities

Late January 2011 – end February, 2011 – Selection of vendor for RFP 02

March, 2011 – July, 2011 – finalizing invoicing with vendor. Submission of 1st invoice.

Late May, 2011 – FCL 01 facilities all live

September – Early October, 2011 – FCL's of additional facilities

November, 2011 – Mid February, 2012 – continued outreach for additional partners

Late February – RFP 03 posted on USAC website; as well as Funding Commitment Letter 02 facilities and Funding Commitment Letter 03 facilities live on WNY RBHN.

Late March, 2012 – Early April, 2012 – Bid Review Committee selection of vendor

Mid – Late April, 2012 – documentation completed for issuance of FCL

Ongoing Processes – review regular program to see facilities that qualify and start processes to add them on to WNY RBHN.



R·AHEC

Rural Area Health Education Center

20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275

*

Fax: 585-786-6280

*

Email: wnyrbhn@r-ahec.org

** New information for the quarterly report appears in the purple, bold, italic font*

Telemedicine Benefits ~ Our facilities have currently just gone live end of 2010 – Mid, 2011. As the facilities continue to go live and the network continues to add partners this information will continue to increase. We are also in the process of bringing up other facilities onto our network. The majority of the facilities that were brought live via RFP 01 were the rural facilities. We currently just received the Funding Commitment Letter 02 for 10 more facilities through RFP 02 as well as our Funding Commitment Letter 03 for 1 additional facility and expect much better communication and access to various entities at that point in time. We are also working on another RFP to be posted in Mid-Late February, 2012 for even more facilities.

While we are continuing to develop the multiple RFP's and receiving Funding Commitment Letters for our network the Western New York Rural Area Health Education Center, Inc. and its Pilot Program Partners are working on the development and framework for evaluating clinical telemedicine and distant health care education applications. Discussions are currently underway between rural and urban partners in developing Pilot Projects for telemedicine and distance health education in preparation for the broadband access and services that will be provided through the FCC Pilot Project. We expect that as our network continues to expand and additional facilities are added on the telemedicine benefits for all partners will continue to grow.

The Below information is based upon project planning and is not actually achieved yet through the network.

A) Explain how the supported network has achieved the goals and objectives outlined in selected participant's Pilot Program Application:

One thing the Pilot Program has provided for the facilities within the network is the broadband that they need at a more affordable cost. Several of the facilities needed more bandwidth and simply couldn't afford it. Through the efforts of the Pilot Program a majority of the facilities have doubled if not tripled the bandwidth that they had and are receiving a subsidy to help them. The network these facilities are participating in is a Multi-Label Protocol Label Switching (MPLS) guaranteeing quality of service and prioritization for all telehealth applications that run over it. Connecting the Rural and Urban facilities through the efforts of this network will ultimately allow the rural communities with telemedicine for patients who would have compromised access.

We are also currently working on convening people across all of upstate NY that are interested in utilizing Telehealth to explore ways in which collaboration can occur to improve effectiveness and lower the costs of technology.

B) Explain how supported network has brought the benefits of innovative telehealth and, in particular, telemedicine services to those areas of the country where the need for those



R·AHEC

Rural Area Health Education Center

20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275

*

Fax: 585-786-6280

*

Email: wnyrbhn@r-ahec.org

** New information for the quarterly report appears in the purple, bold, italic font*

benefits is most acute:.. This broadband network is connecting multiple healthcare providers for the implementation of telehealth applications. This network impacts telehealth to rural areas because currently rural areas have limited access to specialist and services of care; the experience logistical, financial and quality of life burdens for them to travel to tertiary care centers that are not available in their areas; a lack of remote monitoring solution linking providers, requiring home/office visits.

C) Explain how the supported network has allowed patients access to critically needed medical specialists in a variety of practices without leaving their homes or communities:

D) Explain how the supported network has allowed health care providers access to government research institutions, and/or academic, public, or private health care institutions that are repositories of medical expertise and information: We are currently expanding and reaching out to additional partners frequently to enable additional health care provider access to the multiple organizations such as government research institutions, academic, public, or private health care institutions that can often be the repositories of medical expertise and information.

E) Explain how the supported network has allowed health care professional to monitor critically ill patients at multiple locations around the clock, provide access to advanced applications in continuing education and research, and/or enhanced the health care community's ability to provide a rapid and coordinated response in the event of a nation crisis.



20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275

*

Fax: 585-786-6280

*

Email: wnyrbhn@r-ahec.org

** New information for the quarterly report appears in the purple, bold, italic font*

HHS Health IT Initiatives

Provide Detail on how the supported network has complied with HHS health IT initiatives:

- A) Explain how the supported network has used health IT systems and products that meet interoperability standards recognized by the HHS Secretary:***
- B) Explain how the supported network has used health IT products certified by the Certification Commission for Healthcare Information Technology:***
- C) Explain how the supported network has supported the Nationwide Health Information Network (NHIN) architecture by coordinating activities with organizations performing NHIN trial implementations:***
- D) Explain how the supported network has used resources available to HHS's Agency for Healthcare Research and Quality (AHRQ) National Resource Center for Health Information Technology:***
- E) Explain how the selected participant has educated themselves concerning the Pandemic and All Hazards Preparedness Act and coordinated with the HHS Assistant Secretary for Public Response as a resource for telehealth inventory and for the implementation of other preparedness and response initiatives:***
- F) Explain how the supported network has used resources available through HHS's Centers for Disease Control and Prevention (CDC) Public Health Information Network (PHIN) to facilitate interoperability with public health and emergency organizations:***

While we are developing the multiple RFP's and receiving Funding Commitment Letters for our network the Western New York Rural Area Health Education Center, Inc. and its Pilot Program Partners are working on the development and framework for evaluating clinical telemedicine and distant health care education applications. Discussions are currently underway and have been continuing between rural and urban partners in developing Pilot Projects for telemedicine and distance health education in preparation for the broadband access and services that will be provided through the FCC Pilot Project. We also continue to apply for grants to assist with leveraging grant where applicable for telemedicine and distance health education. We expect that as our network continues to expand and additional facilities are added on the telemedicine benefits for all partners will continue to grow.



W. AHEC
Rural Area Health Education Center

20 Duncan Street, PO Box 152, Warsaw, NY 14569

Phone: 585-786-6275

*

Fax: 585-786-6280

*

Email: wnyrbhn@r-ahec.org

** New information for the quarterly report appears in the purple, bold, italic font*

HHS & CDC

Explain how the selected participants coordinated in the use of their health care networks with the Department of Health and Human Services (HHS) and, in particular, with its Centers for Disease Control and Prevention (CDC) in instances of national, regional, or local public health emergencies (e.g., pandemics, bioterrorism). In such instances, where feasible, explain how selected participants provided access to their supported networks to HHS, including CDC, and other public health officials.

While we are developing the multiple RFP's and receiving Funding Commitment Letters for our network the Western New York Rural Area Health Education Center, Inc. and its Pilot Program Partners are working on the development and framework for evaluating clinical telemedicine and distant health care education applications. Discussions are currently underway between rural and urban partners in developing Pilot Projects for telemedicine and distance health education in preparation for the broadband access and services that will be provided through the FCC Pilot Project. We expect that as our network continues to expand and additional facilities are added on the telemedicine benefits for all partners will continue to grow.
