大成 DENTONS

Todd D. Daubert
Partner

todd.daubert@dentons.com
D +1 202 408 6458

Dentons US LLP
1900 K Street, NW
Washington, DC 20006
United States

大成 **Salans FMC SNR Denton McKenna Long**
dentons.com

July 27, 2016

VIA ECFS

Ms. Marlene H. Dortch
Secretary
Federal Communications Commission
445 12th Street, SW
Washington, DC 20554

Re: ***Telephone Number Portability, et al.***
CC Docket No. 95-116; WC Docket Nos. 09-109 and 07-149

Dear Secretary Dortch:

The North American Portability Management LLC (the "NAPM LLC"), by its attorneys, hereby files a written summary of the NAPM LLC's status updates to the Federal Communications Commission ("FCC" or "Commission") regarding the transition from the current local number portability administrator ("LNPA"), Neustar, to the new LNPA, Telcordia d/b/a iconectiv (the "Report"). This Report updates the FCC, the public, and all interested stakeholders regarding transition activities to date in accordance with the requirements of the LNPA Selection Order[1] and guidance received from the FCC on June 24, 2015. The NAPM LLC will continue to file written updates of this Report with the FCC at the end of each month until transition is complete.

Transition Oversight Plan

The latest version of the Transition Oversight Plan ("TOP"), dated August 31, 2015, is published on the public portion of the NAPM LLC's website at www.NAPMLLC.org.

Stakeholder Outreach and Education

A Transition Outreach and Education Plan ("TOEP") was developed and finalized with the oversight of the FCC, and is included as an Exhibit in the amended TOP filed on August 31, 2015. The TOM has hosted five LNPA Transition Outreach ("LTO") webcasts since December 2015. In addition, there have been several in-person events for stakeholders to share perspectives and ask questions about the LNPA transition. The content and notes from the webcast meetings have been posted on the NAPM LLC's website at the following URL: https://www.napmllc.org/pages/home.aspx.

Transition Oversight Manager

The TOM continued to advance the objectives of the LNPA transition program in June. Accomplishments included:

- Confirmed the June deliveries of NPAC data from the current LNPA to the incoming LNPA for development and testing of the new NPAC system;

---

1 *Telcordia Technologies, Inc. Petition to Reform Amendment 57 and to Order a Competitive Bidding Process for Number Portability Administration et al.*, Order, WC Docket Nos. 07-149, 09-109, CC Docket No. 95-116, ¶¶ 158-59 (rel. Mar. 27, 2015) (*LNPA Selection Order*).

- Gained alignment between the current and the incoming LNPAs on the process to manage clarifications in the June and July deliveries of NPAC data;
- Submitted a memorandum to the Neustar Pooling Administrator ("PA") recommending the development of an independent PA Change Order (CO 3A) that addresses only the development of the PAS NPAC API specification;
- Updated the Pooling parallel operations approach document to further clarify the requirements to support development of the revised PA Change Order;
- Updated the parallel operations approach document for SPID/MUMP Migrations to address feedback from the current LNPA;
- Updated the contingency rollback governance process to address NAPM LLC feedback;
- Conducted the TOEP webcast on 6/21/2016 attended by 258 participants, replay available at https://event.webcasts.com/starthere.jsp?ei=1106539;
- Conducted the first TOEP public-safety in-person event adjacent to the National Emergency Number Association ("NENA") conference in Indianapolis, IN on 6/13/2016 and 6/14/2016;
- Presented the TOM transition update at the North American Numbering Council ("NANC") meeting on 6/30/2016;

The TOM conducts weekly meetings with the NAPM LLC Transition Team, iconectiv and Neustar to coordinate activities and communication among the parties and address ad hoc issues as they arise. These working meetings are used to identify, discuss and close tasks (A.K.A. action items) required to advance the project objectives. The graph below depicts the progress achieved in addressing these action items since the last monthly report.

Transition Action Item Progress (6/1/16 through 6/30/16)

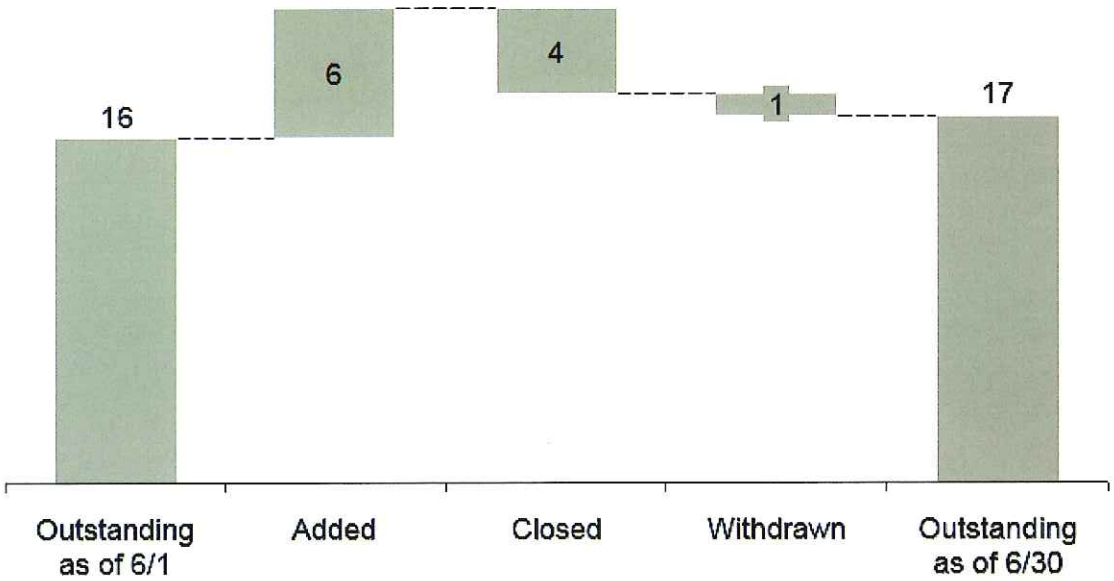

The TOM continues to track identified LNPA transition risks including the summary program risks below:

- Dates for key milestones are dependent on the completion of the iconectiv master services agreement, and completion of this agreement is extending significantly beyond previous expectations; and

- Agreement on key transition requirements is necessary in order to finalize the approach to important transition plans, including:

  - The timing and sequencing of key transition activities, such as ancillary services; and

  - The finalization of an approach for LNPA transition contingency rollback.

Negotiations With iconectiv

On July 25, 2016, the FCC released a final decision approving the recommendation of the NANC that iconectiv serve as the next LNPA and the terms and conditions of the draft Master Services Agreement ("MSA") that the NAPM LLC and iconectiv had previously submitted to the FCC.[2] The NAPM LLC and iconectiv intend to execute the MSA and update the key milestones in accordance with the FCC's approval.

Negotiations With Neustar

Neustar began billing industry service providers on their December 2015 monthly Statement of Work ("SOW") invoices for transition service support billable since July 2015, consistent with the terms of SOW 97.

Please contact the undersigned if you have any questions or would like any additional information about the issues discussed herein.

Sincerely,

Partner

100473915\V-2

---

2 *See Telcordia Technologies, Inc. Petition to Reform Amendment 57 and to Order a Competitive Bidding Process for Number Portability Administration et al.*, Order, WC Docket Nos. 07-149, 09-109, CC Docket No. 95-116 (rel. July 27, 2015) (*LNPA Approval Order*).
