Exhibit 1: BellSouth Batch Hot Cut Timeline Dated March 5, 2003
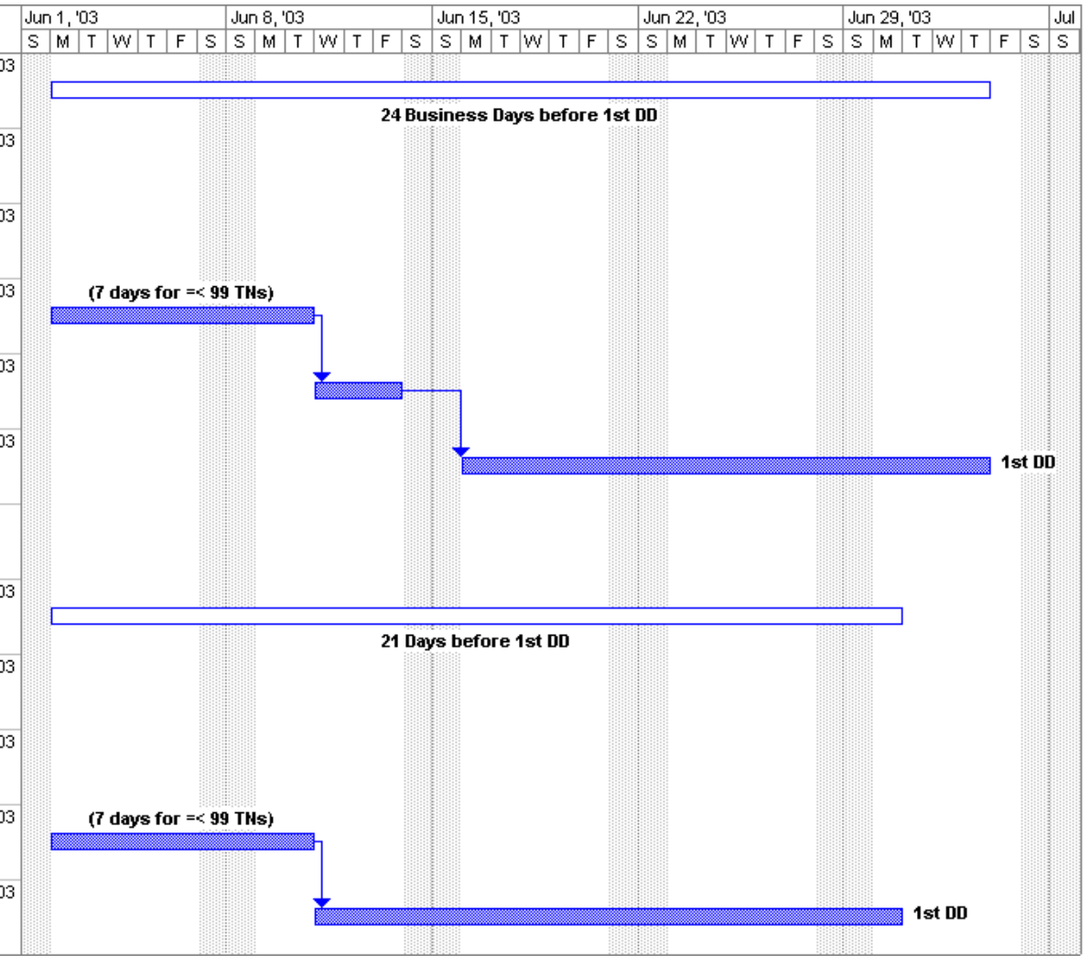
ID	Task Name	Duration	Start	Finish
1	**New Schedule (as of 3/30/03)**	24 days	Mon 6/2/03	Thu 7/3/03
2	Project Manager receives TN Spreadsheet	0 days	Mon 6/2/03	Mon 6/2/03
3	Verify accuracy and pass on to SPOC	0 days	Mon 6/2/03	Mon 6/2/03
4	SPOC provides DD with earliest being 24 days from PM receipt of TN SS	7 days	Mon 6/2/03	Tue 6/10/03
5	CLEC updates BULK LSR with DDs and submits electronically to BellSouth (LCSC)	3 days	Wed 6/11/03	Fri 6/13/03
6	Earliest DD	14 days	Mon 6/16/03	Thu 7/3/03
7				
8	**Old Schedule at time of conference (3/5/03) Revised 3/30/03**	21 days	Mon 6/2/03	Mon 6/30/03
9	Project Manager receives TN Spreadsheet	0 days	Mon 6/2/03	Mon 6/2/03
10	Verify accuracy and pass on to SPOC	0 days	Mon 6/2/03	Mon 6/2/03
11	SPOC provides DD with earliest being 21 days from PM receipt of TN SS	7 days	Mon 6/2/03	Tue 6/10/03
12	Earliest DD	14 days	Wed 6/11/03	Mon 6/30/03
